

THENCE NORTH 42° 58' 15" EAST 330.00 FEET TO THE TRUE POINT OF BEGINNING.

THENCE DEPARTING SAID PARALLEL LINE NORTH 43° 22' 1911 EAST, 90.00 FEET; ALONG SAID NORTHWESTERLY LINE TO THE POINT OF BEGINNING, BY FINAL ORDER OF CONDEMNATION RECORDED JUNE 4, 2004 IN INSTRUMENT NO. 20040635405, RECORDS OF MARICOPA COUNTY, ARIZONA.

1. WEATHER INFORMATION AND STORM PREDICTIONS CAN BE OBTAINED BY CALLING THE NATIONAL WEATHER SERVICE - PHOENIX WEATHER FORECAST OFFICE AT (602) 275-0073 OR BY VISITING THE NATIONAL WEATHER SERVICE WEBSITE AT [HTTP://WWW.WRHI.NOAA.GOV/PSR/](http://www.wrhi.noaa.gov/PSR/)
2. PERMANENT EROSION CONTROL MEASURES SHALL BE INSTALLED AS AREAS ARE DETERMINED TO BE COMPLETE.
3. ALL DRAINAGE INLETS RECEIVING RUNOFF FROM DISTURBED SOIL AREAS SHALL BE PROTECTED WITH AN APPROVED SEDIMENT TRAP INLET PROTECTION MEASURE OR BMP.
4. A COPY OF THE APPROVED GRADING & DRAINAGE PLAN FOR THIS PROJECT, TOGETHER WITH A COPY OF THE NOTICE OF INTENT (NOI) AND THIS STORM WATER POLLUTION PREVENTION PLAN (SWPPP), SHALL BE MAINTAINED ON THE SITE AND AVAILABLE FOR REVIEW AT ALL TIMES. THOSE ELEMENTS OF THE GRADING & DRAINAGE PLAN PERTINENT TO OR REFERENCED ON THE STORM WATER POLLUTION PREVENTION PLAN (SWPPP) SHALL BE CONSIDERED A PART OF THE SWPPP.
5. THE NOTICE OF INTENT (NOI) SHALL BE COMPLETED AND SUBMITTED TO THE ARIZONA DEPARTMENT OF ENVIRONMENTAL QUALITY (ADEQ) AND THE CITY OF SURPRISE AT LEAST FORTY-EIGHT (48) HOURS PRIOR TO ANY CONSTRUCTION ACTIVITY.
6. THE STORM WATER POLLUTION PREVENTION PLAN (SWPPP) AND RELATED RECORDS SHALL BE MADE AVAILABLE UPON REQUEST TO THE ARIZONA DEPARTMENT OF ENVIRONMENTAL QUALITY (ADEQ) AND THE CITY OF SURPRISE.
7. THE OWNER OR DESIGNATED CONTRACTOR SHALL OBTAIN A DUST CONTROL PERMIT FROM THE MARICOPA COUNTY AIR QUALITY DEPARTMENT. MEASURE SHALL BE PERFORMED AS REQUIRED BY THE PERMIT TO PREVENT EXCESS DUST AS INCORPORATED INTO THIS STORM WATER POLLUTION PREVENTION PLAN (SWPPP).
8. THE OWNER OR DESIGNATED CONTRACTOR SHALL AMEND THIS PLAN AS REQUIRED FOR EVENTS, DESIGN CHANGES AND CONSTRUCTION METHODS. DICTATE. ALL MODIFICATIONS TO THIS PLAN SHALL BE SUBMITTED TO THE CITY OF SURPRISE ENGINEERING SERVICES FOR REVIEW AND ACCEPTANCE PRIOR TO IMPLEMENTATION.


9. THE IMPLEMENTATION OF THESE PLANS, AND THE CONSTRUCTION, MAINTENANCE, REPLACEMENT, AND UPGRADES OF THESE FACILITIES IS THE RESPONSIBILITY OF THE OWNER OR DESIGNATED CONTRACTOR UNTIL ALL CONSTRUCTION HAS BEEN APPROVED AND NOTICE OF TERMINATION (NOT) HAS BEEN SUBMITTED TO THE ARIZONA DEPARTMENT OF ENVIRONMENTAL QUALITY (ADEQ) AND THE CITY OF SURPRISE.
10. THE FACILITIES SHOWN ON THIS PLAN SHALL BE CONSTRUCTED IN CONJUNCTION WITH ALL CLEARING AND GRADING ACTIVITIES IN SUCH A MANNER AS TO ENSURE THAT SEDIMENT-LOADED WATER DOES NOT LEAVE THE PROJECT SITE, ENTER INTO THE DRAINAGE SYSTEM, OR VIOLATE APPLICABLE WATER QUALITY STANDARDS. ADDITIONALLY, THE FACILITIES SHALL BE INSTALLED AND OPERATIONAL PRIOR TO ANY GRADING OR LAND CLEARING ACTIVITIES.
11. WHEN POSSIBLE, MAINTAIN ANY NATURALLY OCCURRING VEGETATION AS A EROSION CONTROL BEST MANAGEMENT PRACTICE (BMP).
12. THE CONTRACTOR TO WHOM THE 'AT-RISK' / FINAL GRADING & DRAINAGE PERMIT WILL BE ISSUED SHALL HAVE THE APPROVED STORM WATER POLLUTION PREVENTION PLAN (SWPPP) ISSUED IN THEIR NAME.
13. THE NOTICE OF INTENT (NOI), THE APPROVED STORM WATER POLLUTION PREVENTION PLAN (SWPPP), AND THE MARICOPA COUNTY AIR QUALITY DEPARTMENT DUST CONTROL PERMIT SHALL BE PROVIDED TO THE CITY OF SURPRISE BEFORE THE GRADING & DRAINAGE PERMIT WILL BE ISSUED.
14. THE OWNER OR DESIGNATED CONTRACTOR OF THE PROJECT SHALL ALSO MAINTAIN RECORDS WITH THE FOLLOWING INFORMATION:
 - A) THE DATES WHEN MAJOR GRADING ACTIVITIES OCCUR IN A PARTICULAR AREA.
 - B) THE DATES WHEN CONSTRUCTION ACTIVITIES CEASE IN A PARTICULAR AREA (TEMPORARILY OR PERMANENTLY).
 - C) THE DATES WHEN AN AREA IS STABILIZED (TEMPORARILY OR PERMANENTLY).
 - D) THE DATES OF ANY MAINTENANCE, REPLACEMENT, OR REMOVAL OF REQUIRED BMP'S HAS OCCURRED.
15. ONCE THE CONSTRUCTION ACTIVITIES HAVE BEEN COMPLETED AND THE SITE HAS MET THE FINAL STABILIZATION REQUIREMENTS OF THE PERMIT, THE AUTHORIZED SITE REPRESENTATIVE SHALL FILE A NOTICE OF TERMINATION (NOT) WITH THE ARIZONA DEPARTMENT OF ENVIRONMENTAL QUALITY (ADEQ)

18. THE PERMITTEE SHALL MAINTAIN ALL RECORDS ON FILE, INCLUDING THE NOTICE OF INTENT (NOI), THE STORM WATER POLLUTION PREVENTION PLAN (SWPPP), THE NOTICE OF TERMINATION (NOT), AND ANY AND ALL INSPECTION REPORTS FOR A MINIMUM OF THREE (3) YEARS FROM THE FROM THE FILING DATE OF THE NOTICE OF TERMINATION (NOT).
17. THE OUTLETS OF ALL SEDIMENT BASINS, TRAPS, AND LOCATIONS OF ARTIFICIALLY CONCENTRATED FLOW SHALL BE PROVIDED WITH OUTLET PROTECTION TO PREVENT EROSION AND SCOUR.
18. THOSE RESPONSIBLE FOR SWPPP PREPARATION, IMPLEMENTATION AND PERMIT COMPLIANCE SHALL BE PROPERLY TRAINED, AND SHALL ATTEND THE PRE-CONSTRUCTION MEETING.
19. A CONCRETE WASHOUT SHALL BE INSTALLED FOR ALL PROJECTS THAT PROPOSE CONCRETE TO BE MIXED ON SITE OR BE DELIVERED FROM A BATCH PLANT. THE CONCRETE WASHOUT SHALL BE LOCATED A MINIMUM OF FIFTY (50) FEET FROM ANY DRAINAGE INFRASTRUCTURE OR NATURAL DRAINAGE FEATURES OR WATER BODIES AND IN CORPORATE AN IMPERMEABLE LINER (6.0 MIL MINIMUM THICKNESS) TO CONTAIN THE REQUIRED VOLUME. ALL DRIED CONCRETE WASTE SHALL BE BROKEN INTO MANAGEABLE PIECES AND DISPOSED OF OFF-SITE AT AN APPROVED DISPOSAL FACILITY.
20. THE CONTRACTOR SHALL HAVE EMERGENCY MATERIALS AND EQUIPMENT ON-SITE FOR UNFORESEEN SITUATIONS, SUCH AS DAMAGE TO UNDERGROUND WATER AND SEWER UTILITIES WHEREBY FLOWS MAY GENERATE EROSION AND SEDIMENT POLLUTION.
21. SEDIMENT AND EROSION CONTROLS MAY BE REMOVED ONLY WHEN CONTRIBUTORY UPSTREAM AREAS BECOME STABILIZED OR MANAGED UPSTREAM AND AS LONG AS SEDIMENT LADEN RUNOFF WILL NOT DISCHARGE FROM THE SITE.
22. THIS PLAN SHALL BE IN EFFECT UNTIL ALL DISTURBED AREAS ARE PERMANENTLY STABILIZED, TRANSFERRED TO NEW OWNERSHIP, OR DEVELOPED UNDER FUTURE PLANS WITH A NEW NOTICE OF INTENT (NOI), SWPPP, AND PERMIT.


1. THE OWNER OR DESIGNATED CONTRACTOR SHALL PERFORM, AT A MINIMUM, A VISUAL INSPECTION OF THE PROJECTION OF THE PROJECT SITE ONCE EVERY SEVEN (7) DAYS AND WITHIN TWENTY-FOUR (24) HOURS OF A RAINFALL


- EVENT GREATER THAN OR EQUAL TO ONE HALF (1/2) INCH. THE OWNER OR DESIGNATED CONTRACTOR SHALL PREPARE A REPORT DOCUMENTING THE FINDINGS OF THE STORM WATER POLLUTION PREVENTION PLAN (SWPPP) CONTROLS AND NOTE ANY EROSION PROBLEM AREAS. THE REPORT IS TO BE SUBMITTED TO THE PUBLIC WORKS DEPARTMENT CONSTRUCTION INSPECTOR FOR REVIEW AND APPROVAL. FACILITIES SHALL BE MAINTAINED AS NECESSARY TO ENSURE THEIR CONTINUED FUNCTIONING. IN ADDITION, ALL TEMPORARY EROSION CONTROLS SHALL BE MAINTAINED IN A SATISFACTORY CONDITION UNTIL SUCH TIME THAT CONSTRUCTION IS COMPLETED. PERMANENT DRAINAGE FACILITIES ARE OPERATIONAL, AND POTENTIAL FOR EROSION HAS BEEN ELIMINATED AS DETERMINED BY THE PUBLIC WORKS DIRECTOR OR DESIGNEE.
2. THE INSPECTION BY THE OWNER OR DESIGNATED CONTRACTOR SHALL INCLUDE, AT A MINIMUM, THE FOLLOWING:
- A) CHECK DISTURBED AREAS AND ANY MATERIAL STORAGE AREAS (IF APPLICABLE) TO THE STORM WATER POLLUTION PREVENTION PLAN (SWPPP) FOR EVIDENCE OF OR THE POTENTIAL FOR DISCHARGE OF POLLUTANTS.
 - B) ENSURE THAT SEDIMENT AND EROSION MEASURES ARE FUNCTIONING AND OPERATING CORRECTLY.
 - C) AT ACCESSIBLE DISCHARGE POINT, DETERMINE WHETHER BMP'S ARE EFFECTIVE IN PREVENTING SIGNIFICANT IMPACTS TO RECEIVING WATERS. WHERE DISCHARGE POINTS ARE INACCESSIBLE OR UNSAFE TO INSPECT, INSPECT DOWNSTREAM AREAS FOR EVIDENCE OF DISCHARGE.
 - D) DOCUMENT SEDIMENT TRACK-OUT AT ALL INGRESS AND EGRESS LOCATIONS LOCATIONS FROM THE PROJECT SITE.
 - E) DOCUMENT ANY REVISIONS TO BMP'S ON THE STORM WATER POLLUTION PREVENTION PLAN (SWPPP) WITHIN SEVEN (7) DAYS OF INSPECTION AND CORRECTION.
 - F) DOCUMENT ANY INCIDENTS OF NON-COMPLIANCE OR CERTIFY THAT THE SITE IS IN COMPLIANCE WITH THE STORM WATER POLLUTION PREVENTION PLAN (SWPPP).
 - G) DOCUMENT ANY ACTIVITY THAT CREATES A NON-STORM WATER DISCHARGE INCLUDING DATE AND TIME, LOCATION, REASON FOR DISCHARGE, AMOUNT OF THE DISCHARGE, BMP MEASURES USED TO MEDIATE THE DISCHARGE, AND BMP'S USED TO PREVENT FURTHER NON-STORM WATER DISCHARGES FROM THE ACTIVITY.

1. PRIOR TO OR IMMEDIATELY FOLLOWING CLEARING & GRUBBING, AND AS PART OF THE INITIAL ROUGH GRADING, ALL RETENTION BASINS SHALL BE CUT TO GRADE. THE BASINS SHALL CONSTITUTE THE REQUIRED SEDIMENT BASINS. GRADES SHALL BE CUT (BERMING OR STRAW BALES MAY ALSO BE PROVIDED) PER THIS PLAN TO ASSURE THAT RUNOFF IS CONVEYED TO THE RETENTION BASINS.
2. A STABILIZED CONSTRUCTION ENTRANCE CONSISTING OF A MINIMUM OF SIX (6) INCHES OF COARSE AGGREGATE SHALL BE INSTALLED AS SHOWN. ALL CONSTRUCTION TRAFFIC SHALL ENTER THROUGH THIS ENTRANCE. THE STABILIZED CONSTRUCTION ENTRANCE SHALL BE RE-GRADED OR REPLACED WHEN IT BECOMES SATURATED OR MATTED WITH SITE SOILS OR SEDIMENT. THE PAVED STREET ADJACENT TO THE CONSTRUCTION ENTRANCE SHALL BE SWEEPED ON A REGULAR BASIS TO REMOVE ANY ACCUMULATED MUD OR DIRT TRACKED FROM THE SITE.
3. ANY DISTURBED AREAS WHERE CONSTRUCTION HAS PERMANENTLY OR TEMPORARILY CEASED SHALL BE STABILIZED TO PREVENT EROSION, AN ACCEPTABLE STABILIZATION METHOD IS HYDROSEEDING AND WATERING. AREAS WHICH WILL BE DISTURBED WITHIN TWENTY-ONE (21) DAYS OF CEASING CONSTRUCTION MAY BE STABILIZED BY WATERING.
4. THE CATCH BASIN LOW POINTS SHALL ALSO ACT AS THE REQUIRED SEDIMENT BASINS FOR THE PROJECT. THEY SHALL BE INSPECTED ON A MONTHLY BASIS AND AFTER EVERY RAIN EVENT. SEDIMENT SHALL BE REMOVED FROM THE BASINS AS NECESSARY TO MAINTAIN A MINIMUM OF SEVENTY-FIVE (75) PERCENT OF REQUIRED CAPACITY OF THE BASIN DURING CONSTRUCTION AND ONE-HUNDRED (100) PERCENT OF REQUIRED CAPACITY POST-CONSTRUCTION.
5. THE SWPP P IS USED TO MAINTAIN ALL ON-SITE STORM WATER POLLUTANTS AND SEDIMENT. HOWEVER, IF ANY OFF-SITE ACCUMULATIONS OF SEDIMENT OR POLLUTANTS OCCUR, IMMEDIATE ACTION SHALL BE REQUIRED TO REMOVE THE ACCUMULATION.

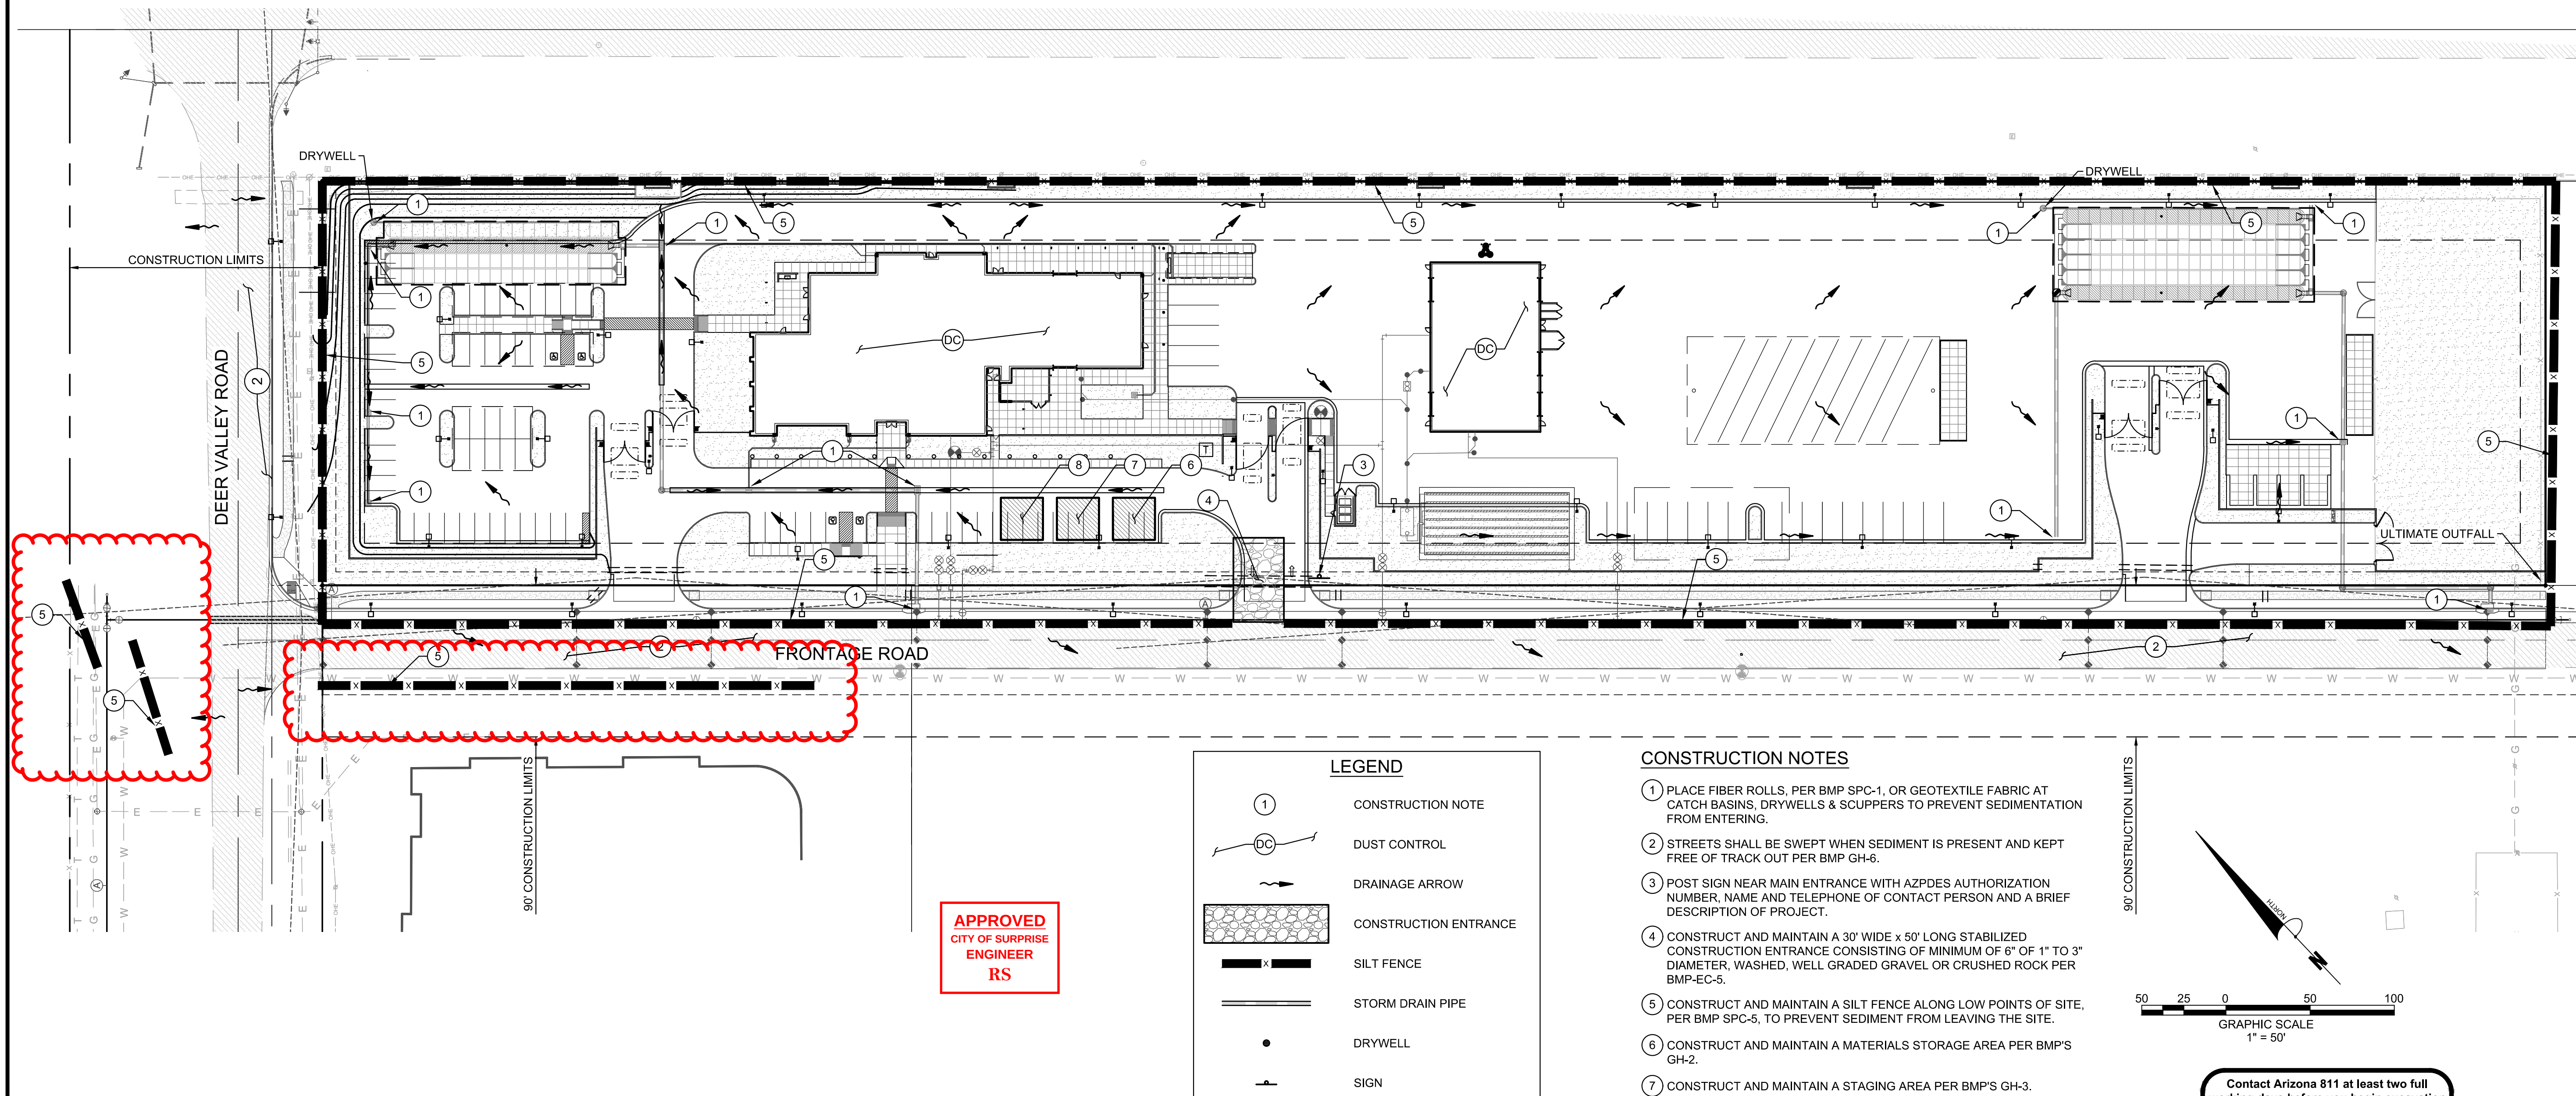


- 1 PLACE FIBER ROLLS, PER BMP SPC-1, OR GEOTEXTILE FABRIC AT CATCH BASINS, DRYWELLS & SCUPPERS TO PREVENT SEDIMENTATION FROM ENTERING.
- 2 STREETS SHALL BE SWEPT WHEN SEDIMENT IS PRESENT AND KEPT FREE OF TRACK OUT PER BMP GH-6.
- 3 POST SIGN NEAR MAIN ENTRANCE WITH AZPDES AUTHORIZATION NUMBER, NAME AND TELEPHONE OF CONTACT PERSON AND A BRIEF DESCRIPTION OF PROJECT.
- 4 CONSTRUCT AND MAINTAIN A 30' WIDE x 50' LONG STABILIZED CONSTRUCTION ENTRANCE CONSISTING OF MINIMUM OF 6" OF 1" TO 3" DIAMETER, WASHED, WELL GRADED GRAVEL OR CRUSHED ROCK PER BMP-EC-5.
- 5 CONSTRUCT AND MAINTAIN A SILT FENCE ALONG LOW POINTS OF SITE, PER BMP SPC-5, TO PREVENT SEDIMENT FROM LEAVING THE SITE.
- 6 CONSTRUCT AND MAINTAIN A MATERIALS STORAGE AREA PER BMP'S GH-2.
- 7 CONSTRUCT AND MAINTAIN A STAGING AREA PER BMP'S GH-3.
- 8 CONSTRUCT AND MAINTAIN A WASHDOWN AREA PER BMP'S GH-4.
- DC APPLY DUST CONTROL MEASURES OVER DISTURBED AREAS PER BMP EC-7.

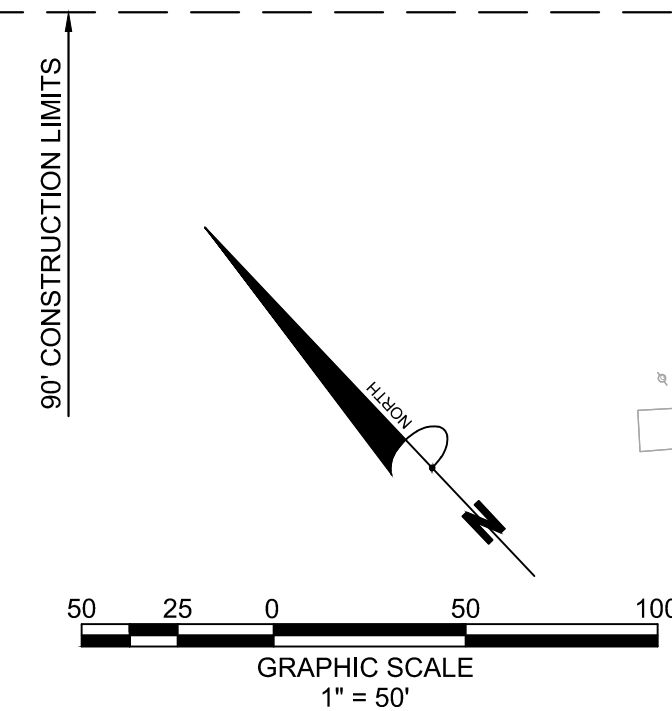




DATE	DESCRIPTION	
JE ESIGN	CF DRAWN	JE CHKD
SCALE	H: 1" = 60' V: N/A	
JOB No. 051568-01-001		
DATE : 11/12/2025		

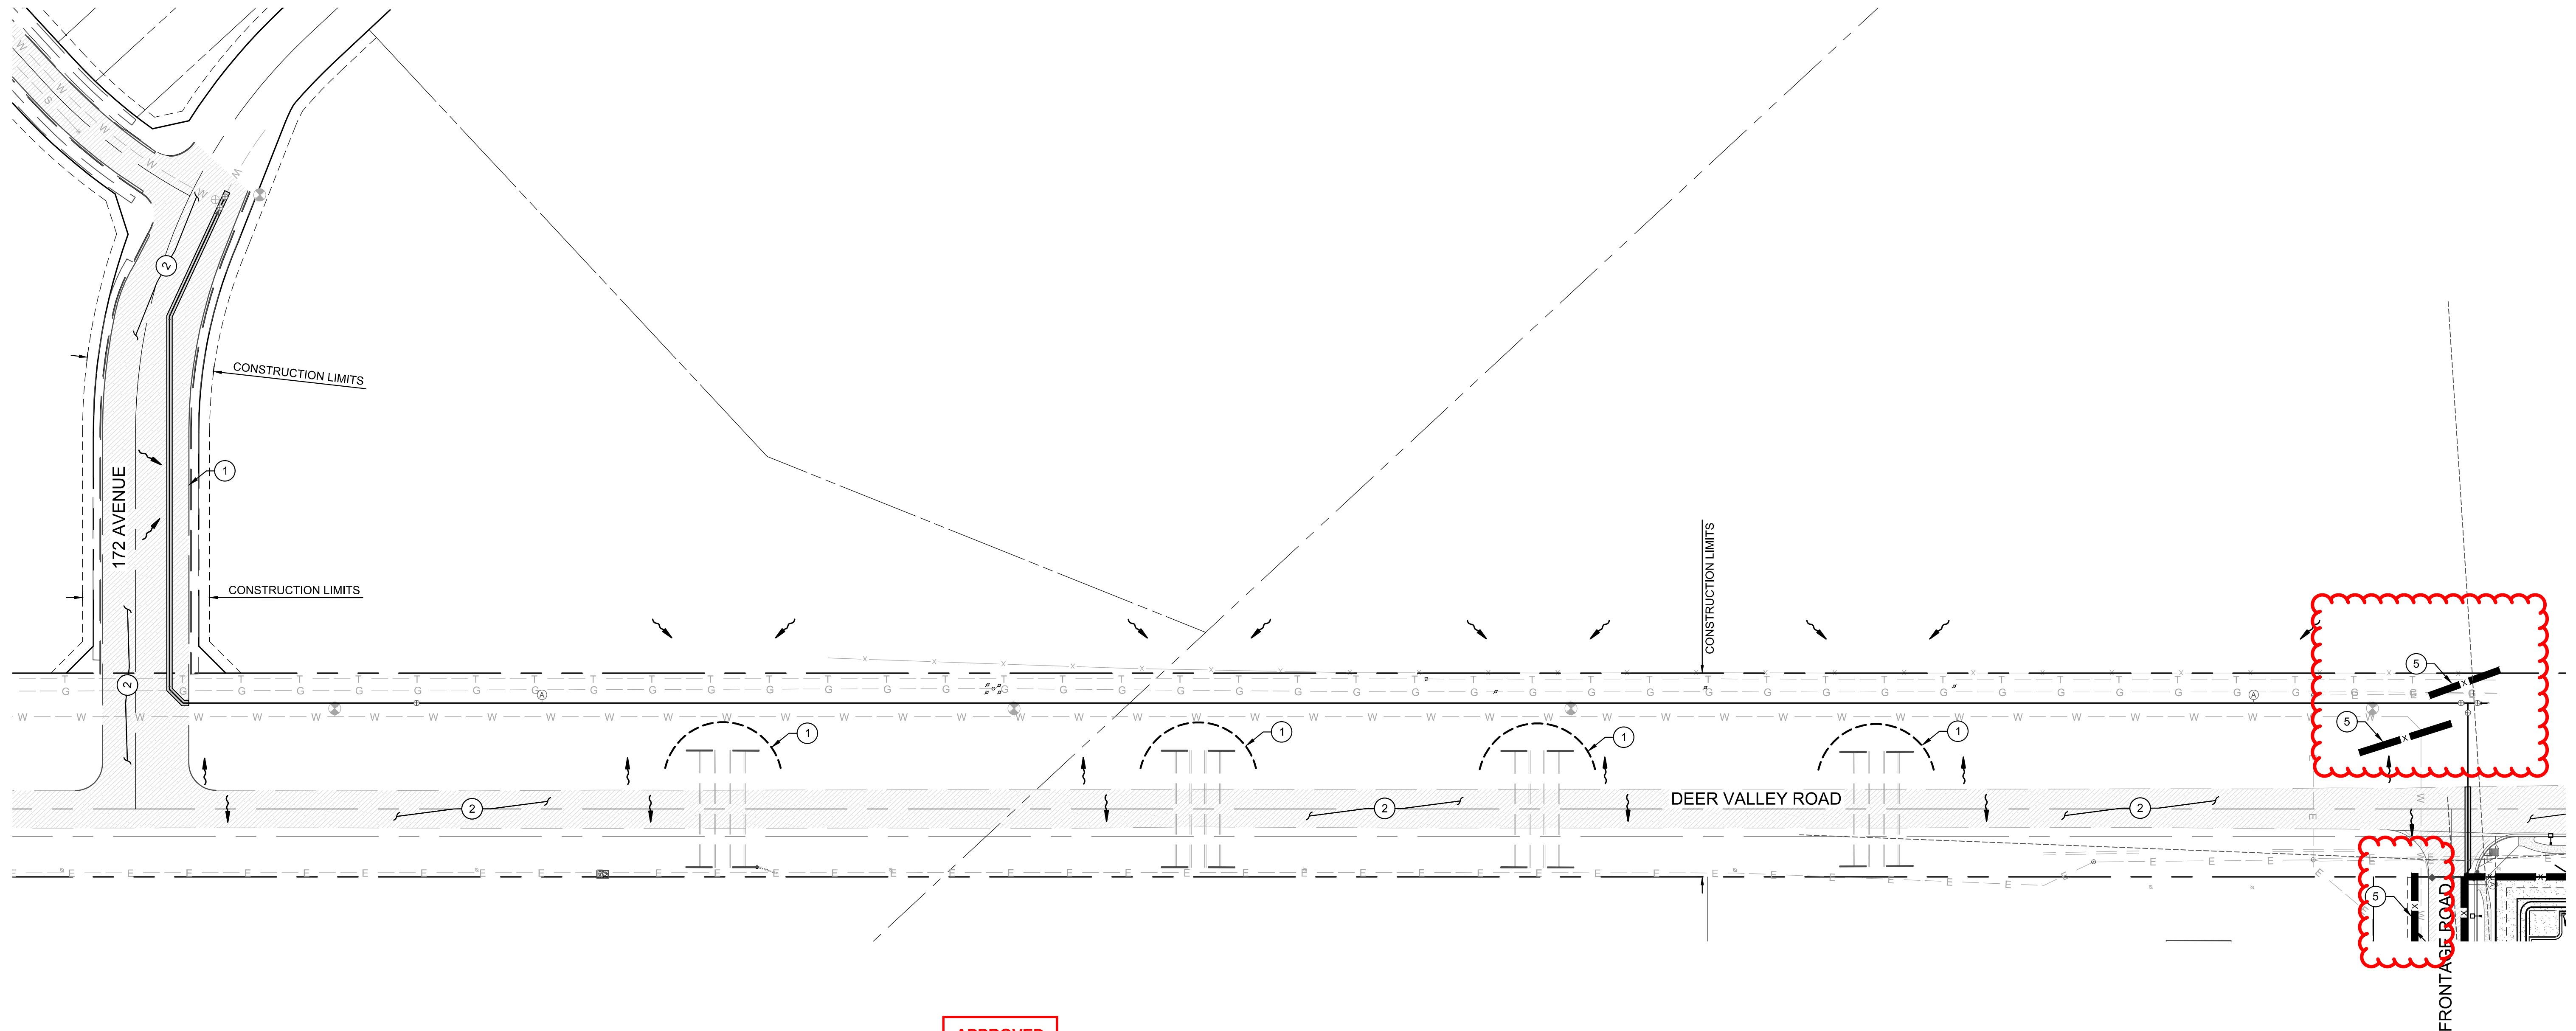


APPROVED
CITY OF SURPRISE
ENGINEER
RS


LEGEND

- | | |
|---|-----------------------|
|  | CONSTRUCTION NOTE |
|  | DUST CONTROL |
|  | DRAINAGE ARROW |
|  | CONSTRUCTION ENTRANCE |
|  | SILT FENCE |
|  | STORM DRAIN PIPE |
|  | DRYWELL |
|  | SIGN |
|  | FIBER ROLLS |

CONSTRUCTION NOTES

- ① PLACE FIBER ROLLS, PER BMP SPC-1, OR GEOTEXTILE FABRIC AT CATCH BASINS, DRYWELLS & SCUPPERS TO PREVENT SEDIMENTATION FROM ENTERING.
- ② STREETS SHALL BE SWEEPED WHEN SEDIMENT IS PRESENT AND KEPT FREE OF TRACK OUT PER BMP GH-6.
- ⑤ CONSTRUCT AND MAINTAIN A SILT FENCE ALONG LOW POINTS OF SITE, PER BMP SPC-5, TO PREVENT SEDIMENT FROM LEAVING THE SITE.

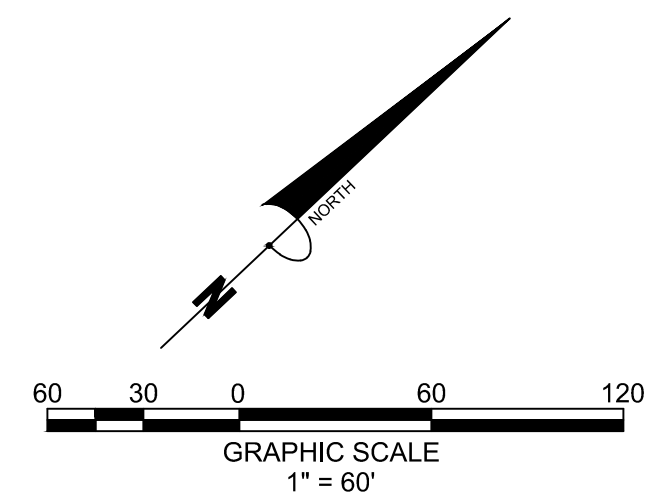




SOUTHWEST GAS CORPORATION
SURPRISE OPERATION CENTER
STORM WATER POLLUTION PREVENTION PLAN
PLAN SHEET

SURPRISE A7

PROJECT NUMBER



PLAN STATUS


[illegible]

DATE	DESCRIPTION	
JE DESIGN	CF DRAWN	JE CHKD
SCALE	H: 1" = 60' V: N/A	
JOB No. 051568-01-001		
DATE : 11/12/2025		

SW4

SHEET 4 OF 4

FS24-0102	
-----------	--

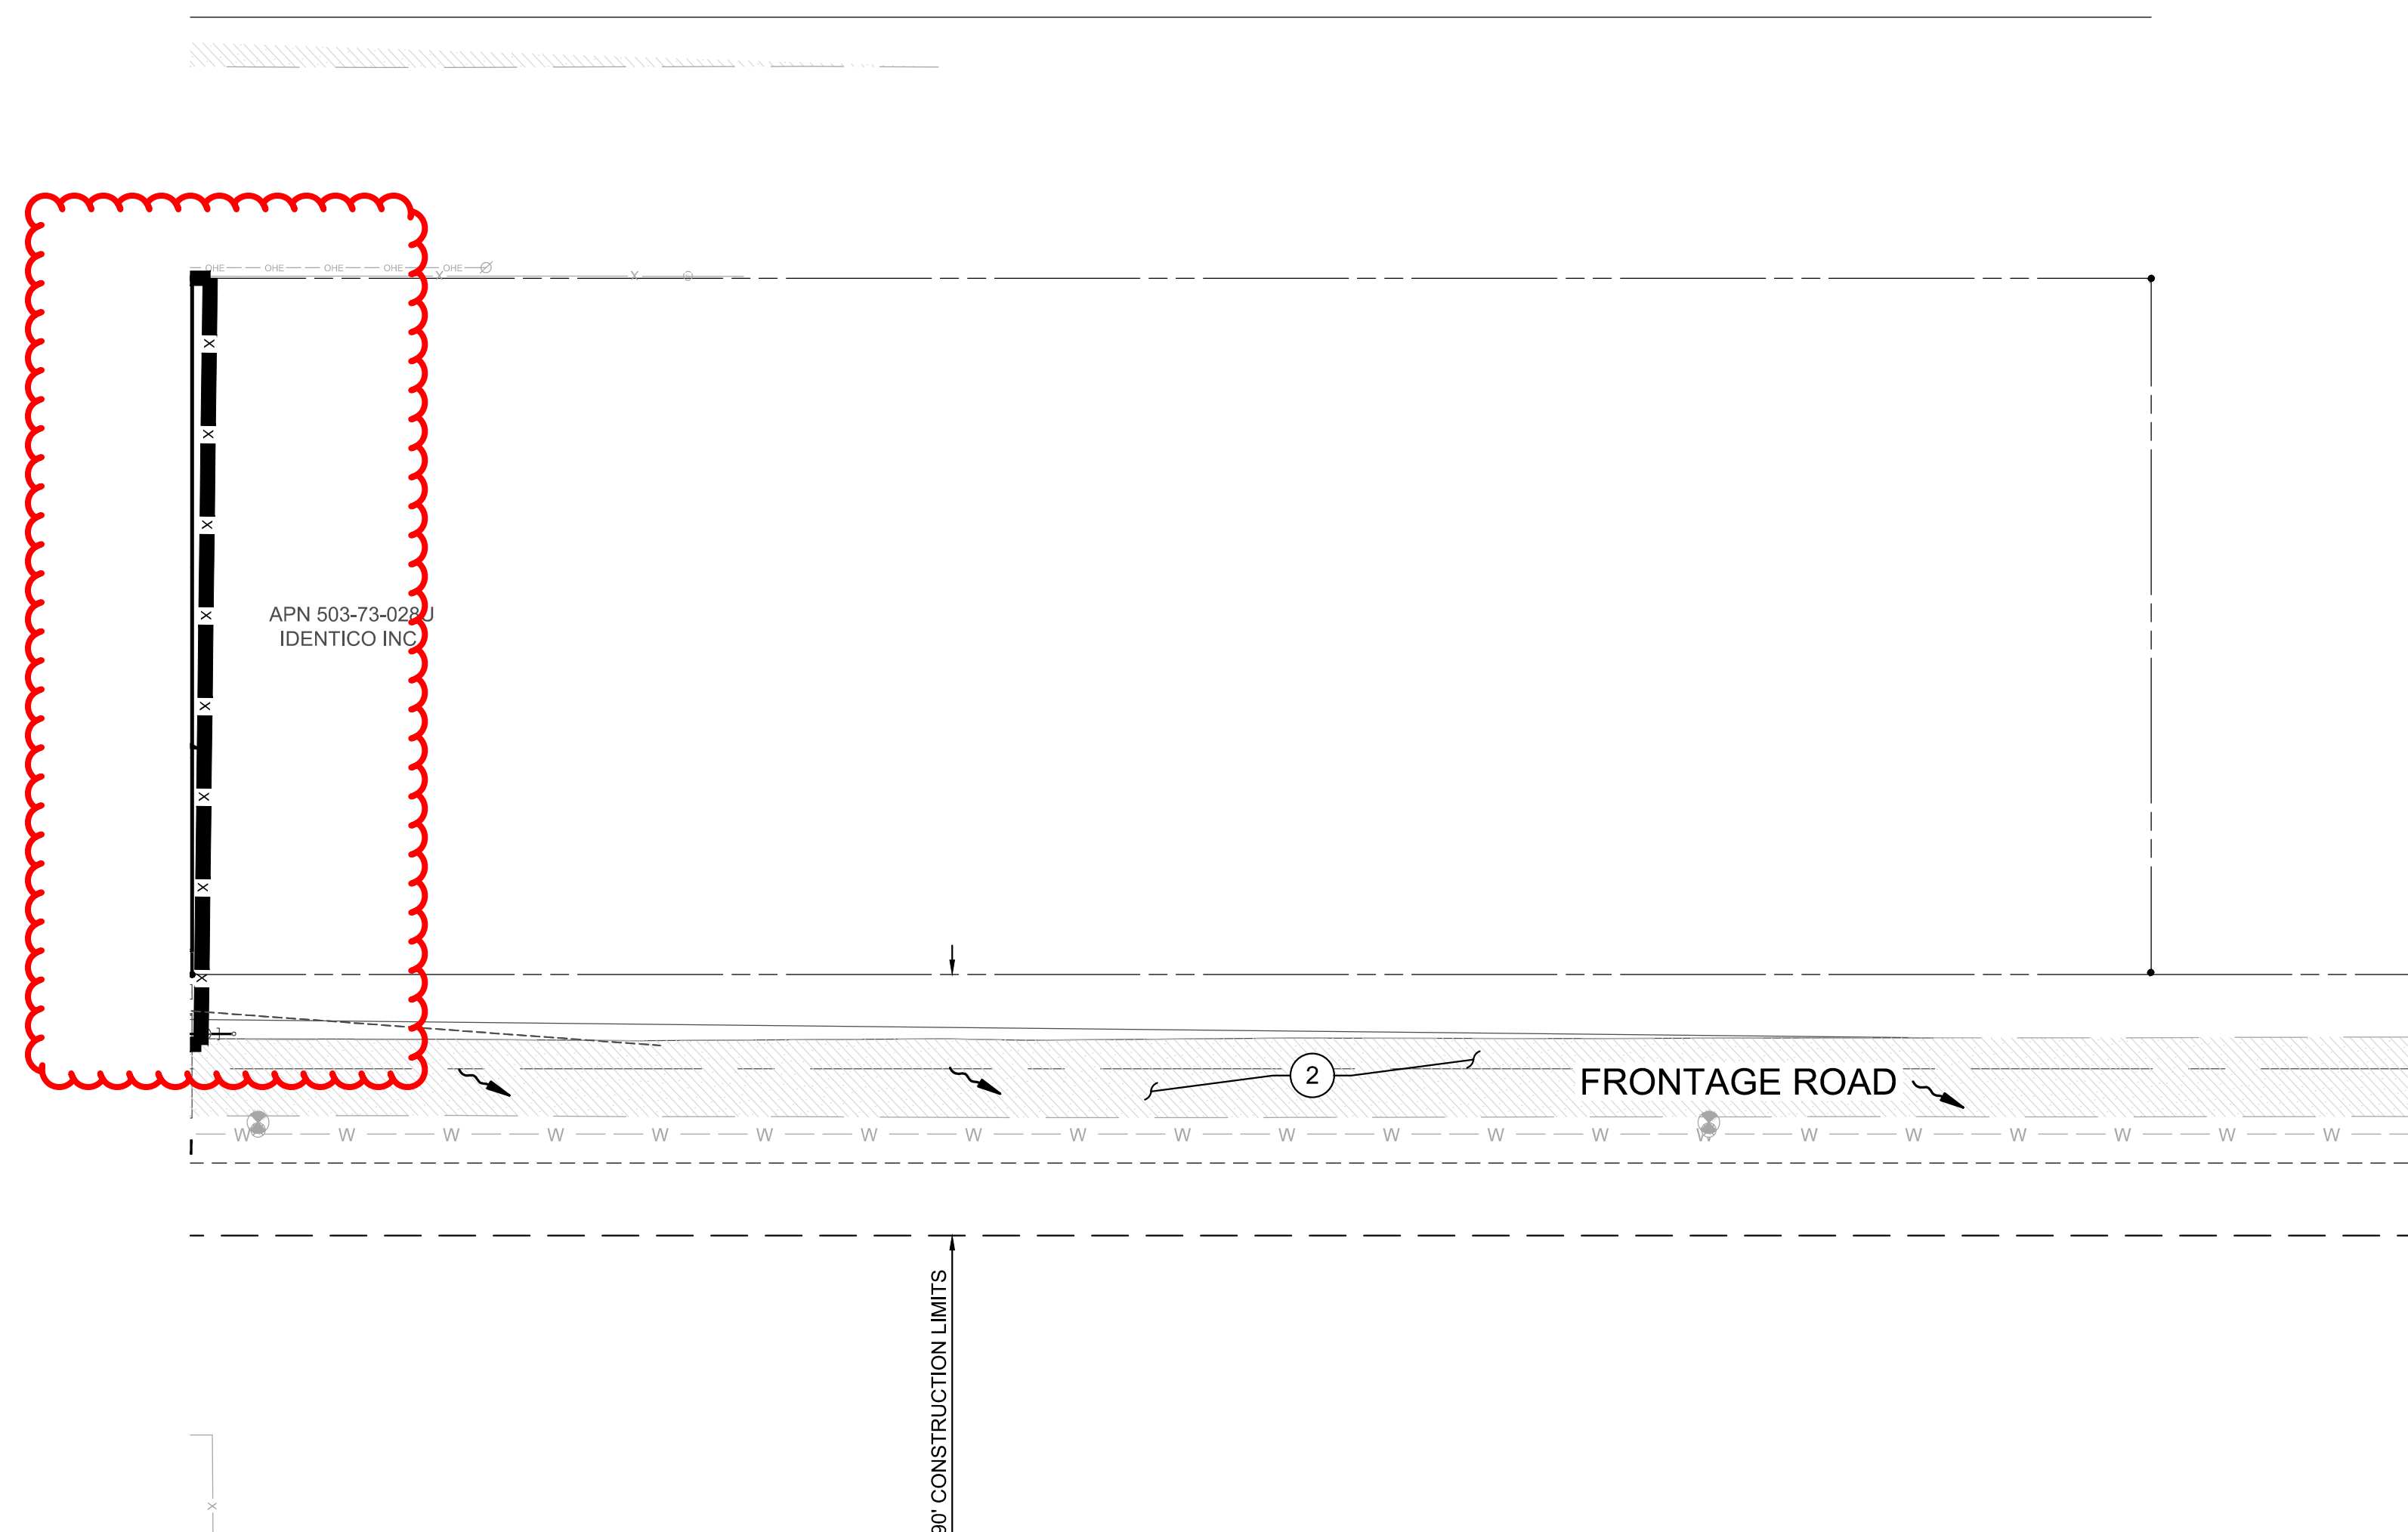


APPROVED
CITY OF SURPRISE
ENGINEER
RS


LEGEND

- | | |
|---|-----------------------|
|  | CONSTRUCTION NOTE |
|  | DUST CONTROL |
|  | DRAINAGE ARROW |
|  | CONSTRUCTION ENTRANCE |
|  | SILT FENCE |
|  | STORM DRAIN PIPE |
|  | DRYWELL |
|  | SIGN |


CONSTRUCTION NOTES

- ② STREETS SHALL BE SWEEPED WHEN SEDIMENT IS PRESENT AND KEPT FREE OF TRACK OUT PER BMP GH-6.

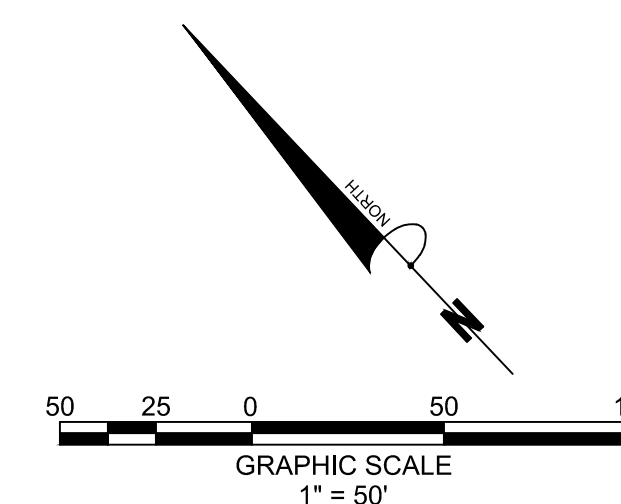

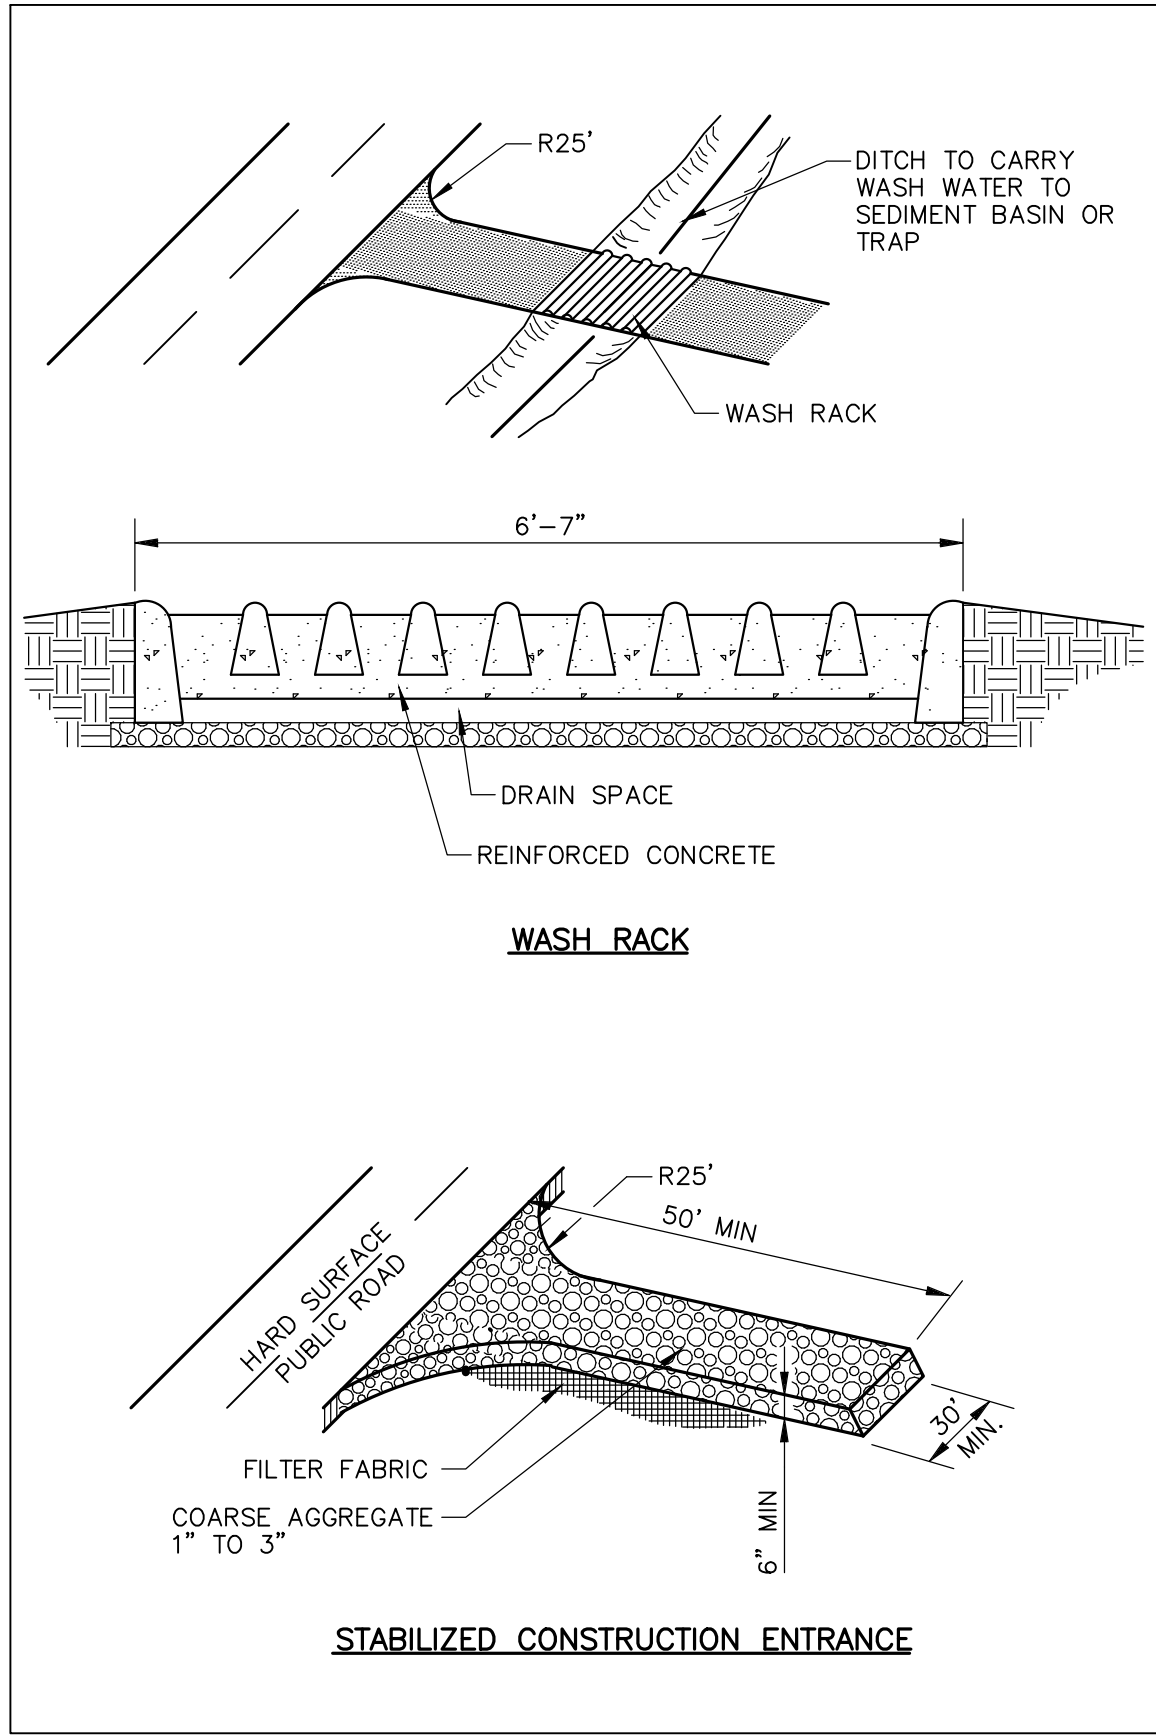


BMP DETAIL EC-5
N.T.S.

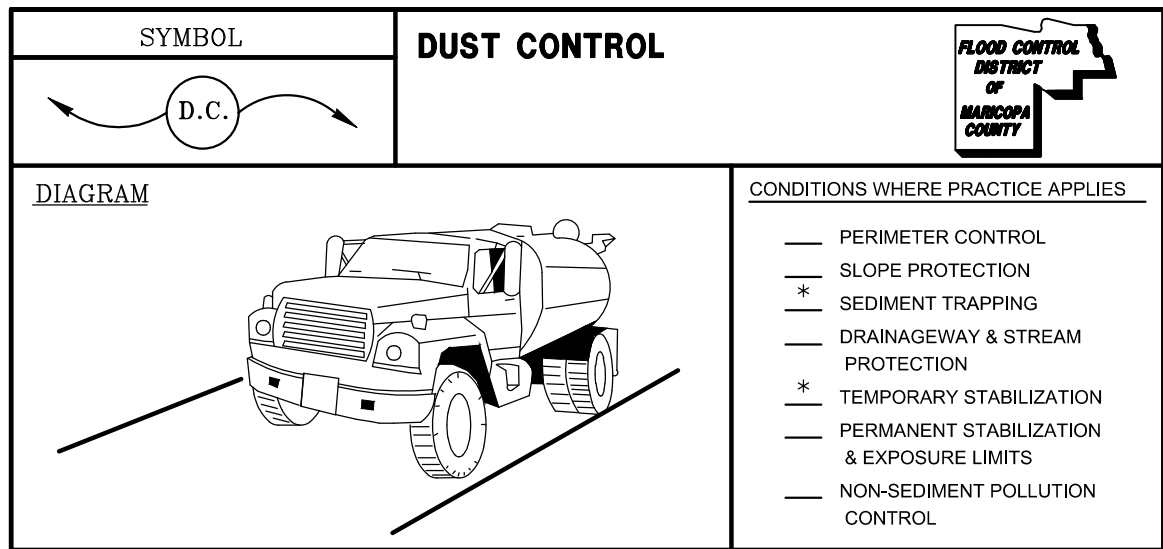

BMP DETAIL EC-7
N.T.S.




BMP DETAIL GH-2
N.T.S.

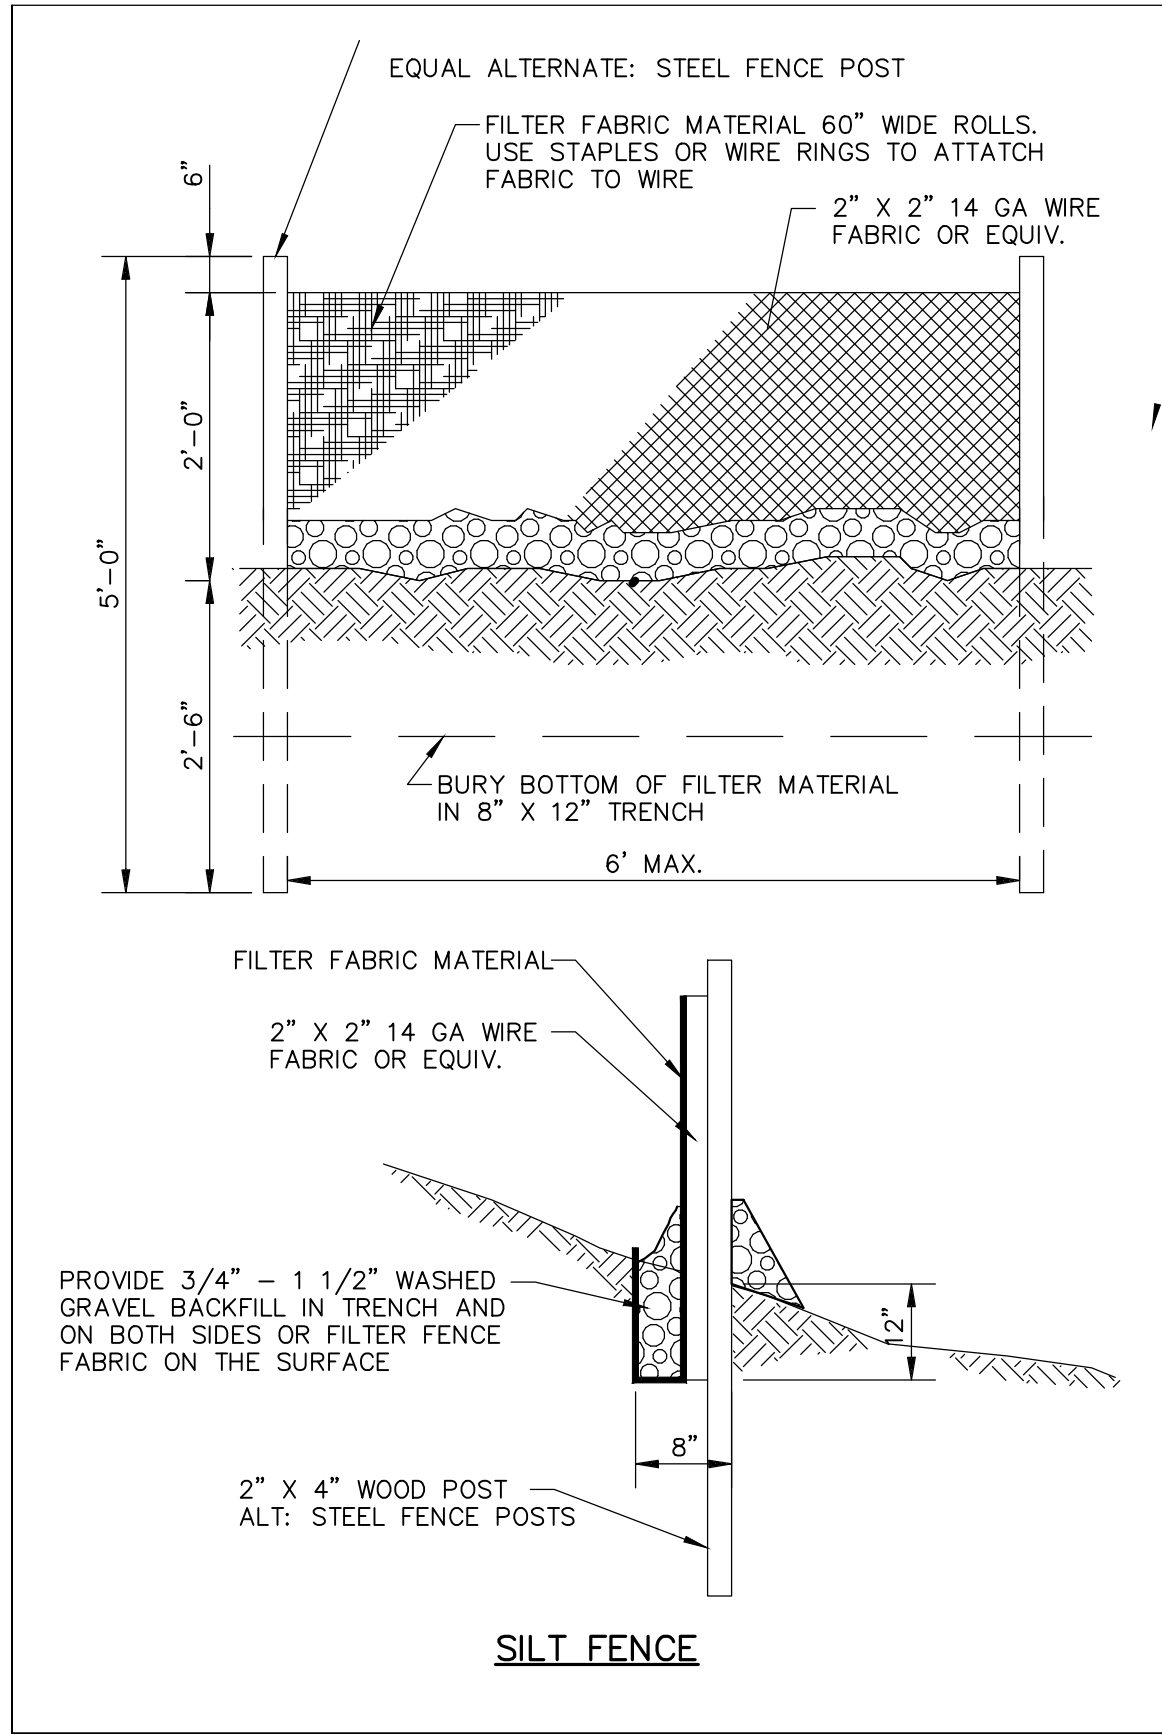

BMP DETAIL SPC-5
N.T.S.


NOTE:

1. ALL MODIFICATIONS WILL BE MARKED ON THE SWPP PLAN WITH DATE OF IMPLEMENTATION. ONCE MODIFIED, A PICTURE OF THE PLAN SHEET SHALL BE SENT TO THE CITY OF SURPRISE ENGINEERING INSPECTOR ASSIGNED TO THE PROJECT.

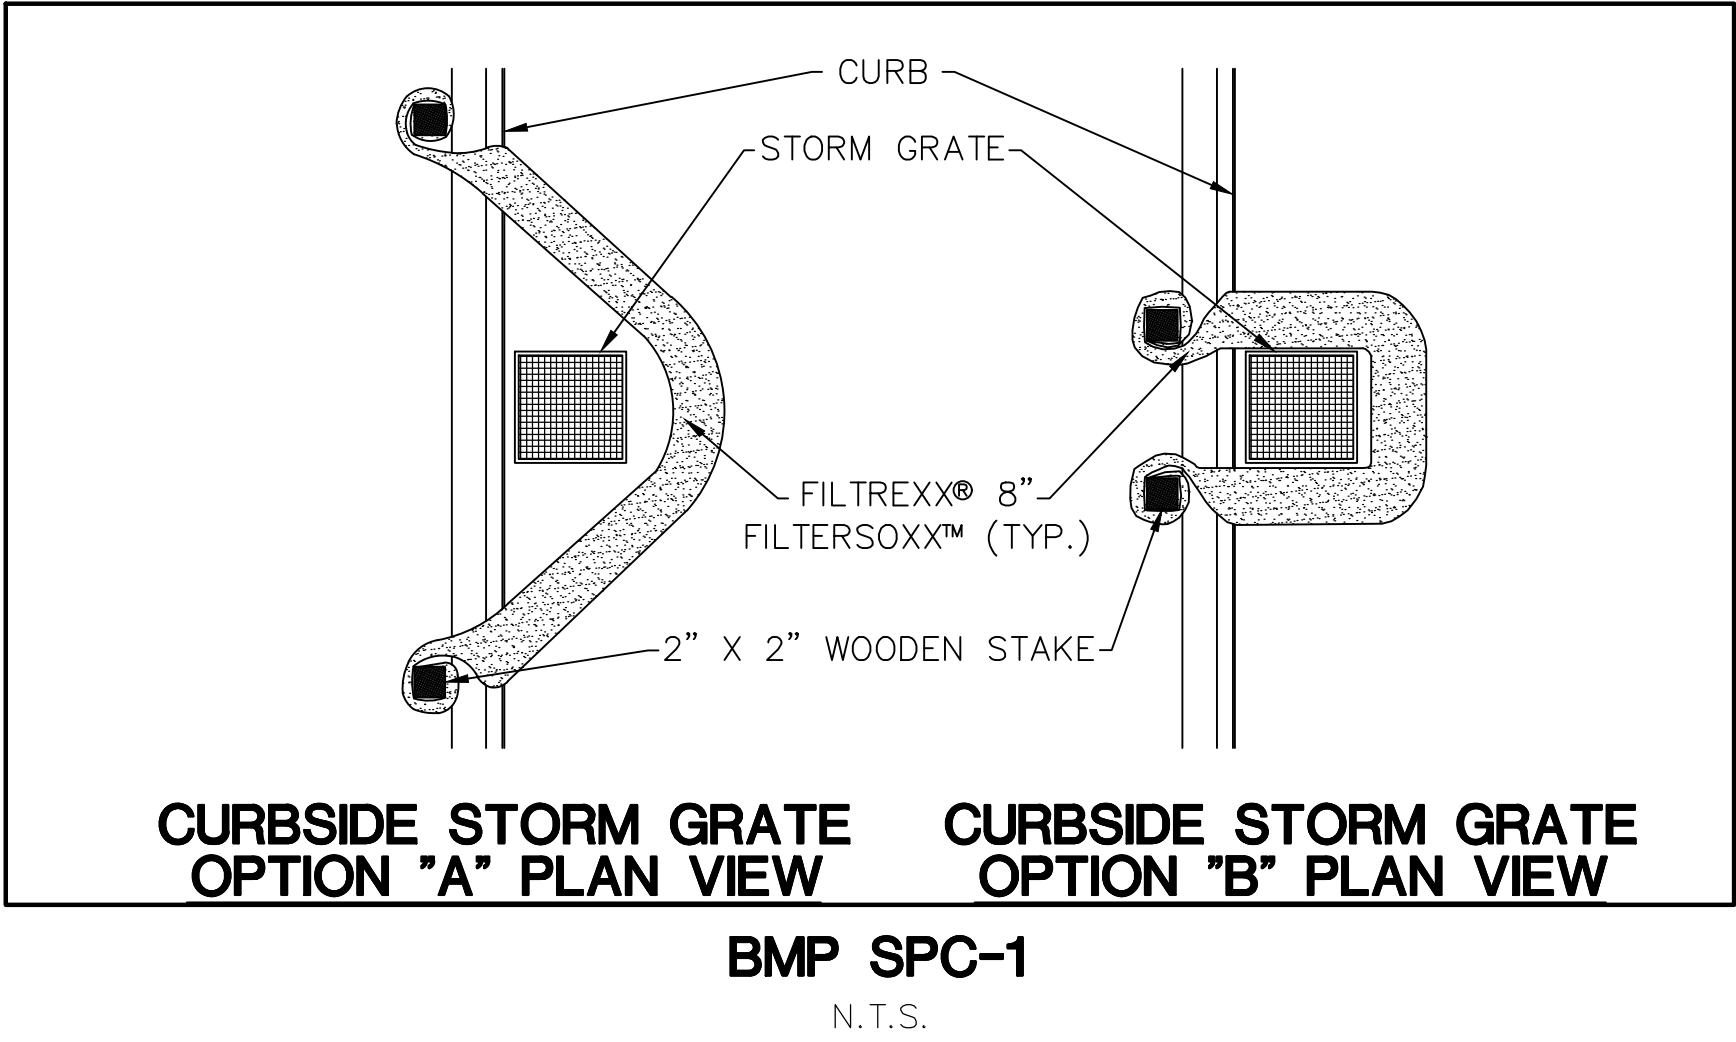

BMP SPC-1
N.T.S.

EQUIPMENT MAINTENANCE PROCEDURES

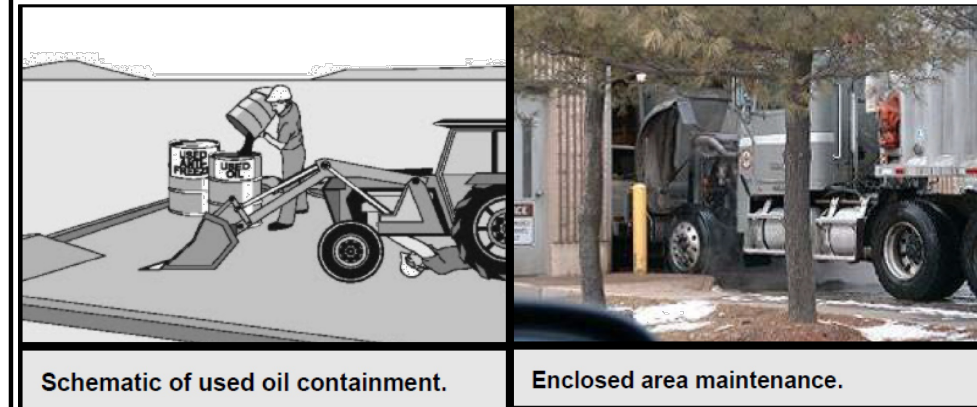

BMP DETAIL GH-3
N.T.S.

Road Sweeping / Trackout Cleaning



BMP DETAIL GH-6
N.T.S.

DESIGNATED WASHDOWN AREAS



BMP DETAIL GH-4
N.T.S.

APPROVED
CITY OF SURPRISE
ENGINEER
RS

Contact Arizona 811 at least two full working days before you begin excavation
ARIZONA811
Call 811 or click Arizona811.com
