



CONTRACT PACKAGE

Project: 25470 Edison and Linear Park

TO: ALL SUBCONTRACTORS

FROM: Tyra Renshaw
trenshaw@lowmountain.com
602.265.2201 x119

DATE: 01/08/26

CONTRACT DUE: Within 7 Business Days

4105 N 20th Street | Suite 205
Phoenix, AZ 85016
P: 602.265.2201 | F: 602.265.7883
www.lowmountain.com

CONTRACT/PO GUIDELINES

Please review this contract package, sign with a **verified digital or handwritten/wet signature** the **EXHIBIT A, MASTER CONTRACT, AND/OR PO** (as applicable), and return to Tyra Renshaw at trenshaw@lowmountain.com **within 7 business days**.

Enclosed you will find the following:

- Exhibits A, B, C, D, E
- Copy of Preliminary Information *for your records*
- Copy of Prime Contractors Certificate (AZ Form 5005) *for your records*

THE COMPLIANCE DOCUMENTS BELOW SHOULD BE SUBMITTED WITH YOUR SIGNED CONTRACT.

FAILURE TO DO SO WILL RESULT IN A HOLD ON PAYMENT OR WILL PREVENT BILLING IN PROCORE.

Signed Exhibit A or PO, and Master Contract (as applicable)

Current W-9

Insurance Certificates (project specific/see Exhibit C included here)

Supplier List (included in this package)

Section 3 Paperwork (see Exhibit E)

SRPMIC Cultural Sensitivity Training Certification

Maricopa County Subcontractor Registration Confirmation

ROC License

<https://www.maricopa.gov/1823/Subcontractor-Registration>

ADDITIONAL DOCUMENTS NEEDED:

Company Contacts Form (included in this package)

 **CONTRACT DUE: Within 7 Business Days**

Please submit contract documents to trenshaw@lowmountain.com

Use the Contract Checklist (last page) provided for your reference to track the documents you submit.

PROCORE TIP:

*Can't locate Exhibit A?
You can export the PDF
any time from your
commitment in Procore.
From the tab labeled
General > Export > PDF*

PROJECT CONTACT INFORMATION

Project Executive :: Wayne Hatch :: whatch@lowmountain.com
change orders, billings, schedule

602.265.2201

Project Manager :: Angela Kamis :: akamis@lowmountain.com
change orders, billings, schedule

602.810.4787

Project Engineer :: Julie Conover :: jconover@lowmountain.com
submittals, RFIs, Procore questions, safety logs

602.265.2201

Accounting :: Aimee Patton :: apatton@lowmountain.com
payments, waivers, insurances, etc.

602.265.2201

Superintendent :: Chris Zollinger :: czollinger@lowmountain.com
on site

602.615.3140

Contracts :: Tyra Renshaw :: trenshaw@lowmountain.com
contract documents

602.265.2201

COMPANY CONTACTS

Complete the Company Contacts form included in this contract package with **all personnel who will be associated with this project** so they may be granted access to Procore. All project management, billing, and payment will be done through Procore.

Return this form to Tyra Renshaw at trenshaw@lowmountain.com.

BILLING PROCEDURES

All billing will be done through Procore and **must be submitted by the closing date of the billing period** (*generally the 25th of the month*). Billing steps are as follows:

Fill out your Subcontractor Schedule of Values

Your SSOV must be entered in Procore after submitting your signed contract
**Projects that are a bid item/quantity project will not have an SSOV*



Approved by PM

An email initiated by the PM via Procore will invite you to bill



Bill for projected work through last day of month



Sign the conditional **and** unconditional waiver in Procore for the net amount of your pay application

Low Mountain will not have access to the unconditional waiver until after payment has been released to you.

**Failure to sign either waiver will delay payment on your pay application.*

Payment of invoices will be through **Procore Pay via ACH**. You must accept the Procore Pay invitation to set up banking information.

All documents needed to release payment will be submitted in Procore and approved:

- ➡ SUPPLIER WAIVERS
- ➡ SAFETY MEETING LOGS
- ➡ WORKFORCE REPORTS *(if project requires)*
- ➡ PAYROLL REPORTS *(if project requires)*
- ➡ COMPLIANCE DOCUMENTS *(as listed in Procore)*

VIEW THE PROGRESS TOWARD PAYMENT RELEASE in Procore as documents are **received** and **approved**.



Receipt of ALL your documents + Payment received from Owner = Subcontractor payment released & deposited via ACH within 24-48 hours

The lien waivers must be requested directly within the Procore monthly invoice.
Supplier waivers must be received with a **verified digital signature** in Procore.

CHANGES TO THE WAIVER, DIGITAL SIGNATURES THAT CANNOT BE AUTHENTICATED, OR WAIVER FORMS OTHER THAN WHAT ARE SUPPLIED WILL NOT BE ACCEPTED.

If a supplier conditional waiver is uploaded, a joint check will be issued in the amount of the conditional waiver and the net amount will be paid to the subcontractor via ACH.

Subcontractors will be **charged \$1 per \$1,000 dollars of contract value** for using **Procore Pay**, with a minimum charge of \$50 and a maximum charge of \$1,000. This fee will be **deducted from the first pay application**.

RETENTION PAYMENT PROCESS



You may **BILL** for payment as soon as **YOUR WORK IS COMPLETED**

PAYMENT will be released when the **PROJECT IS COMPLETE** and **PER THE CONTRACT TERMS**

EMAIL TIP:

When emailing about a project, include the project name in the subject line.

✦ SAFETY LOGS

Compliance with our safety plan requires that **SAFETY LOGS** be submitted weekly for each week you are on the job site. There is no document we provide for this, nor is there a set format. Google search 'Toolbox Talks' for sample forms or provide a log with your company name, date of the meeting, safety topic, and the names of attendees. In order to receive payment, these must be submitted.

Submit weekly Safety Logs to Julie Conover at jconover@lowmountain.com.

✦ DAVIS BACON/PREVAILING WAGE

Davis Bacon projects require that **PAYROLL REPORTS** be submitted weekly to City of Phoenix via **LCP Tracker**. Payroll reports should be submitted **no later than the Monday following the week the payroll was processed**. Payroll reports will be **required to release payment**. The *wage determination* for the project can be found in the *specification* section of the project in Procore. The subcontractor has the responsibility to determine if they have a position for which there is no wage determination and submit the SF1444 form to request a wage determination (*we will supply the form upon request*).

Submit weekly Payroll Reports via LCP Tracker.

✦ SRPMIC CST


The Salt River Pima-Maricopa Indian Community (SRPMIC or Community) sponsors free online Cultural Sensitivity Training (CST) to development and construction personnel. The purpose of the CST is to provide "rules for the road" for construction and development in SRPMIC and is intended to preserve the Community's rich cultural heritage. The training consists of an online video, followed by a short test, and is available in English and Spanish.

It's important to note that the SRPMIC has extensive laws and ordinances that must be followed when conducting construction and development related activities within the boundaries of the Community. Developers, contractors and subcontractors must follow all regulations and laws related to the protection of the Community's cultural and archaeological resources. The CST will provide critical information needed to ensure the protection, preservation, and respectful treatment of these resources.

Subcontractors must have a **CURRENT** certification sticker **at least two weeks prior** to your onsite schedule. Register for the month you plan to attend the training and take the quiz online. Upon passing the quiz, you will receive a certification sticker and you will need to complete the CST Training Tracker (Excel file emailed with your contract) then submit the Excel file to **City of Phoenix**.

Register for the training using this link: <https://srpmic-cst-registration.corsizio.com/>

Please Note: If you have a prior certification sticker but it expires before you will be on the project site, you will need to take the CST again and submit the CST Training Tracker Excel file **before entering the project site**.



FINAL RETENTION BILLING PROCESS

Subcontractor

When you have **completed** your work on the project, you will need to create a **Final Retention Invoice**.

The PM will provide you with a **billing invitation**.

1

Create an invoice

2

For the fields indicated below, **enter** the following:


Invoice # → **FINAL RETENTION**

Billing Type → **FINAL BILLING**

3

In the Schedule of Values, move the scroll bar to view the **TOTAL RETAINAGE RELEASED** column. **Type** in the *same dollar amount* from the **TOTAL RETAINAGE** column on the right.

Continue this process with each line below until the **TOTAL RETAINAGE** column reflects **\$0.00**.

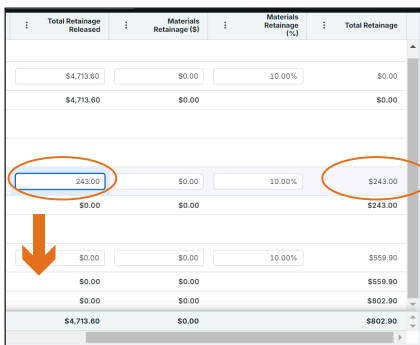

The screenshot shows a table with four columns: Total Retainage Released, Materials Retainage (\$), Materials Retainage (%), and Total Retainage. The first row has values: \$4,713.60, \$0.00, 10.00%, and \$0.00. The second row has values: \$4,713.60, \$0.00, 10.00%, and \$0.00. The third row has values: 243.00, \$0.00, 10.00%, and \$243.00. The fourth row has values: \$0.00, \$0.00, 10.00%, and \$243.00. An orange arrow points down from the third row to the fourth row. The fifth row has values: \$0.00, \$0.00, 10.00%, and \$559.90. The sixth row has values: \$0.00, \$0.00, 10.00%, and \$559.90. The seventh row has values: \$0.00, \$0.00, 10.00%, and \$802.90. The eighth row has values: \$4,713.60, \$0.00, 10.00%, and \$802.90. The values 243.00 and \$243.00 are circled in orange.

4

Click the orange **SAVE** button at the bottom.

5

Next, **select** the **LIEN RIGHTS** tab from your commitment page. Sign both the **CONDITIONAL** and **UNCONDITIONAL FINAL WAIVERS** within the invoice.

Click—Sign—Print—Upload

For subtiers, you will **upload** the **UNCONDITIONAL FINAL WAIVER** using the template we have provided.

The owner will only accept waivers with an authenticated digital signature with verification showing on the certificate.

6


When payment is received from the owner, you will receive an email from Aimee Patton.

You **MUST** use the waiver templates we provide.

An **authenticated digital signature** is an encrypted stamp that confirms the validity and authenticity of the digital document. This may be added in programs such as DocuSign, Adobe, Bluebeam.

No exceptions will be made for other signature types.

NO PAYMENTS are made **until** retention is released at the **end of the project** and per contract terms.

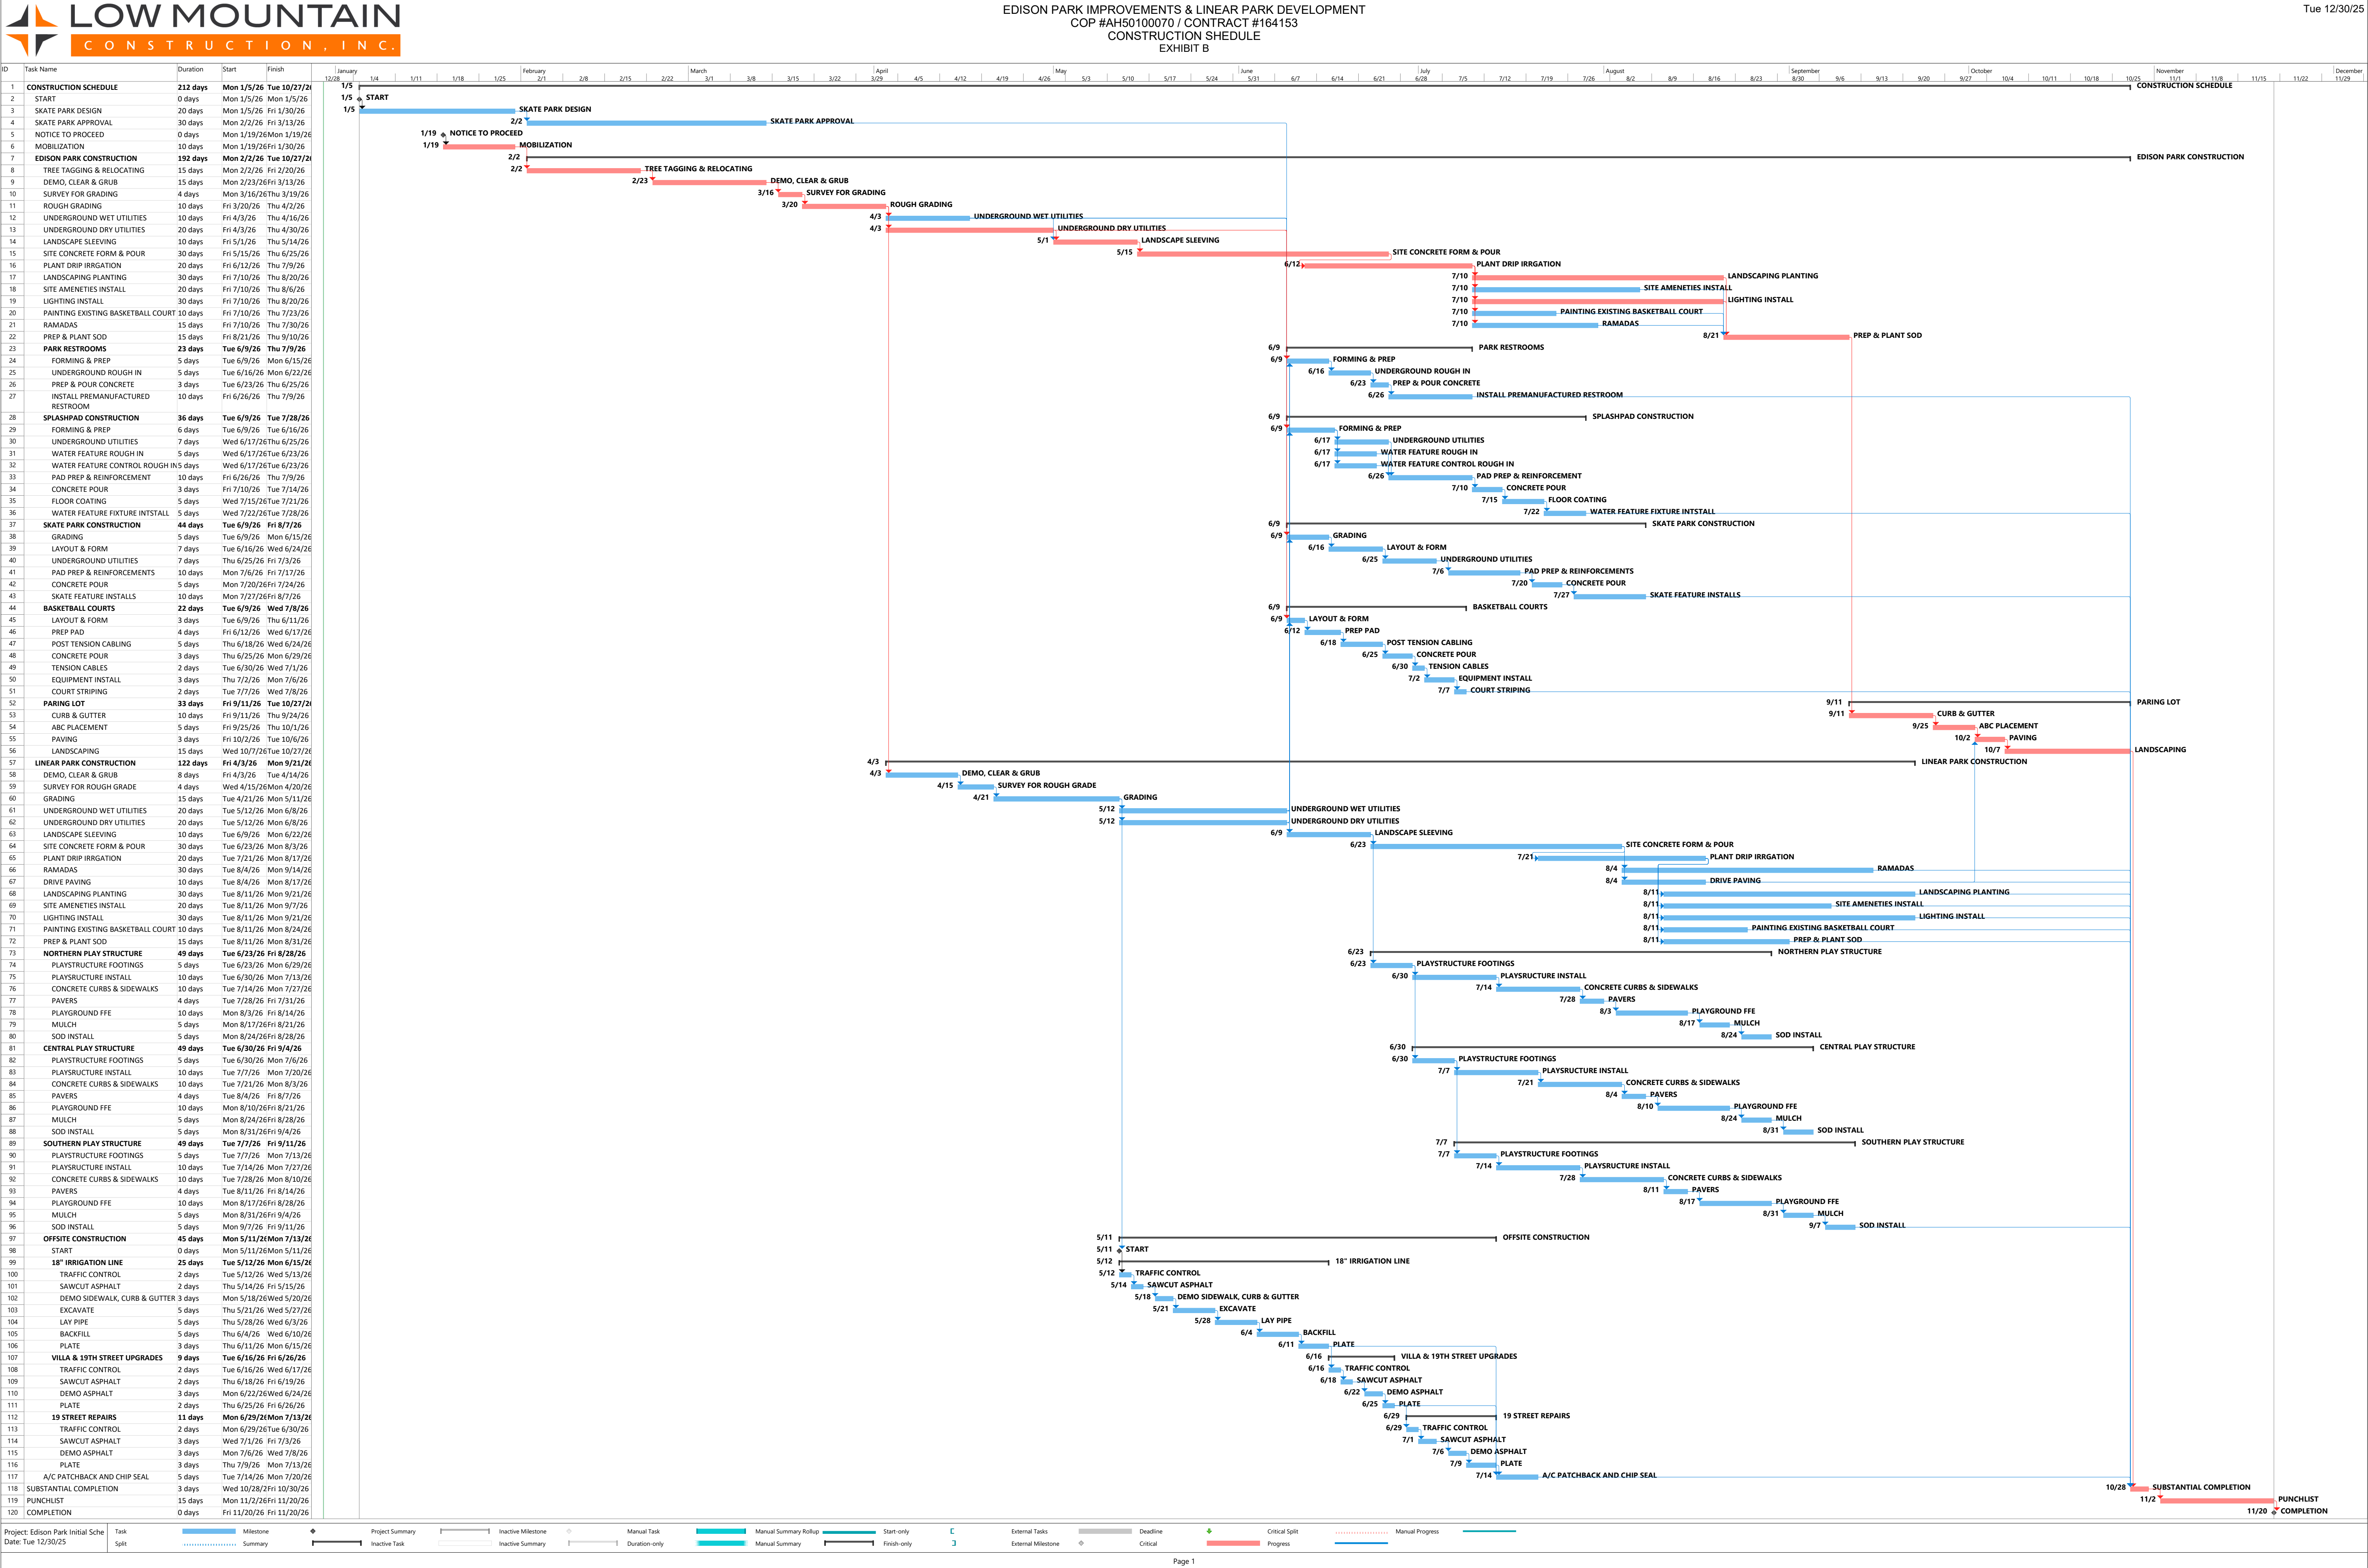

TO: All Subcontractors/Vendors

Prior to commencing any work or services on behalf of **Low Mountain Construction, Inc.** we require that the contractor or vendor provide us with a certificate of insurance for the following lines of insurance:

- ➡ COMMERCIAL GENERAL LIABILITY
- ➡ COMMERCIAL AUTOMOBILE
- ➡ WORKERS COMPENSATION


Failure to meet these requirements constitutes breach of contract and may cause delay or forfeiture of payment for services rendered.

COMMERCIAL GENERAL LIABILITY section must include **minimum limits of \$1,000,000 each occurrence and \$2,000,000 aggregates.** Furthermore, *Low Mountain Construction, Inc.* is to be named as *Additional Insured* for all work performed for or on behalf of Low Mountain Construction, Inc. *No exclusions shall apply for EIFS.*

SAMPLE VERBIAGE: **(Project Name Here)**—Low Mountain Construction, Inc. is named as additional insured on a primary and Non-contributory basis for the General Liability policies. Waiver of Subrogation is included for General Liability and Workers Compensation Policies.

AUTOMOBILE section must provide coverage for any auto or all owned autos and hired and non-owned autos, with limits of not less than **\$1,000,000 per accident.**

WORKERS COMPENSATION section must provide statutory limits for all agents, employees, and volunteers of the contractor or vendor.

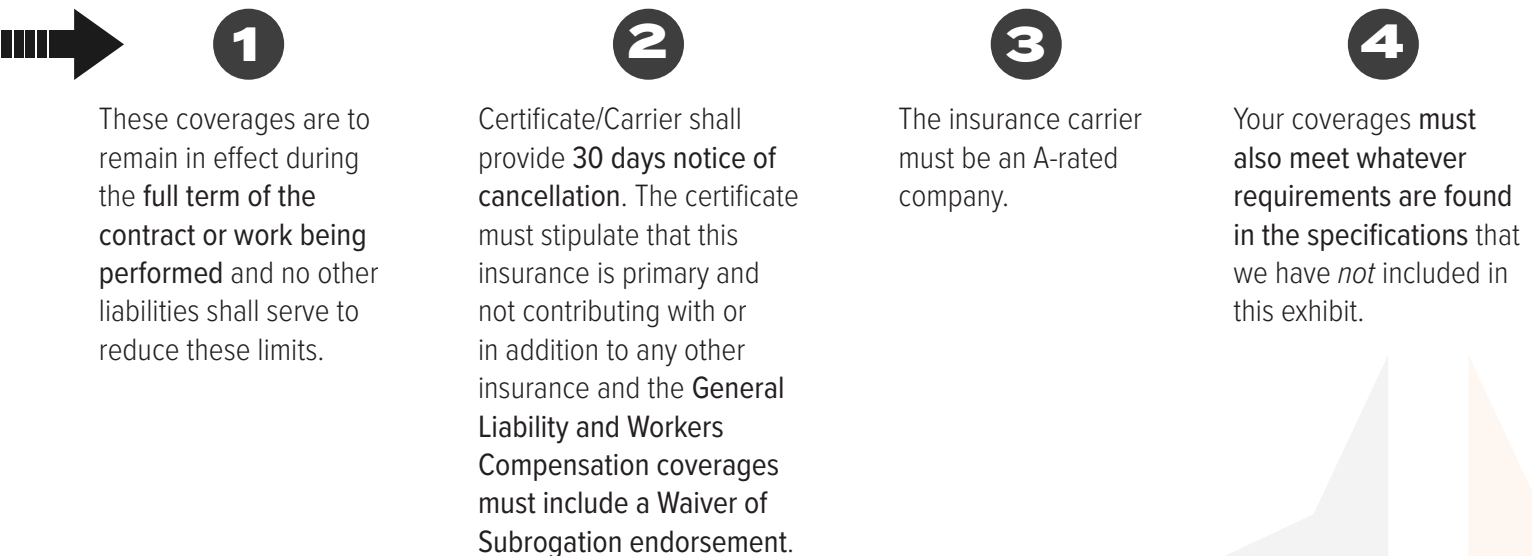

CERTIFICATE OF INSURANCE					ISSUE DATE (MM/DD/YY)
PRODUCER ABC Insurance Co. 123 E. Any Street Hometown, State		THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW.			
		COMPANIES AFFORDING COVERAGE			
		COMPANY LETTER	A	ABC Insurance Co.	
		COMPANY LETTER	B	ABC Insurance Co.	
INSURED ABC Subcontractor 123 E. Any Street Hometown, State		COMPANY LETTER	C	ABC Insurance Co.	
		COMPANY LETTER	D		
COVERAGES					
THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THIS POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.					
CO LTR	TYPE OF INSURANCE	POLICY NUMBER	POLICY EFFECTIVE DATE (MM/DD/YY)	POLICY EXPIRATION DATE (MM/DD/YY)	ALL LIMITS IN THOUSANDS
	GENERAL LIABILITY ☒ COMMERCIAL GENERAL LIABILITY ☐ CLAIMS MADE ☒ OCCUR. POLICY FORM/EDITION <u>CG0001 (10/93)</u> ☒ NO DEDUCTIBLE APPLIES UNLESS INDICATED HERE: \$_____ ☐ OWNER'S & CONTRACTORS PROT. ☐ PER JOB/PER LOC AGG ☒ NO EXCLUSION for EIFS ☐ STOP GAP				GENERAL AGGREGATE \$2,000 PRODUCTS-COMP/OP AGG \$2,000 PERSONAL & ADV. INJURY \$1,000 EACH OCCURRENCE \$1,000 FIRE DAMAGE (Any one fire) \$ 50 MED EXPENSE (Any one person) \$ 5 STOP GAP \$
	AUTOMOBILE ☒ ANY AUTO ☐ ALL OWNED AUTOS ☐ SCHEDULED AUTOS ☐ HIRED AUTOS ☐ NON-OWNED AUTOS				COMBINED SINGLE LIMIT \$1,000 BODILY INJURY (Per person) \$ BODILY INJURY Per accident) \$ PROPERTY DAMAGE \$
	EXCESS LIABILITY ☐ UMBRELLA FORM ☐ OTHER THAN UMBRELLA FORM				EACH OCCURRENCE \$ AGGREGATE \$
	WORKERS COMPENSATION AND EMPLOYERS LIABILITY				STATUTORY \$100 EACH ACCIDENT \$500 DISEASE - POLICY LIMIT \$100 DISEASE - EACH EMPLOYEE
DESCRIPTION OF OPERATIONS/LOCATIONS/VEHICLES/SPECIAL ITEMS (Project Name Here)-Low Mountain Construction Inc. is named as additional insured on a primary and Non-contributory basis for the General Liability policies. Waiver of Subrogation is included for General Liability and Workers Compensation Policies.					
CERTIFICATE HOLDER Low Mountain Construction, Inc. 4105 N. 20 th Street, Suite 205 Phoenix, AZ 85016		CANCELLATION SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELED BEFORE THE EXPIRATION DATE THEREOF, THE ISSUING COMPANY WILL ENDEAVOR TO MAIL <u>30</u> DAYS WRITTEN NOTICE TO THE CERTIFICATE HOLDER NAMED TO THE LEFT, BUT FAILURE TO MAIL SUCH NOTICE SHALL IMPOSE NO OBLIGATION OR LIABILITY OF ANY KIND UPON THE COMPANY, ITS AGENTS OR REPRESENTATIVES.			
		AUTHORIZED REPRESENTATIVE			

END OF EXHIBIT C



EXHIBIT D

PLANS AND SPECIFICATIONS

Plans and specifications, beginning next page.

Current Drawings

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
19th St Linear Park - General					
001	19TH ST LINEAR PARK COVER SHEET	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
19th St Linear Park - Civil					
CLP1.0	GRADING & DRAINAGE COVER SHEET	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CLP1.1	GRADING & DRAINAGE NOTES	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CLP2.1	DEMOLITION PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CLP2.2	DEMOLITION PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CLP2.3	DEMOLITION PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CLP3.1	HORIZONTAL CONTROL PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CLP3.2	HORIZONTAL CONTROL PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CLP3.3	HORIZONTAL CONTROL PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CLP4.1	GRADING & DRAINAGE PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CLP4.2	GRADING & DRAINAGE PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CLP4.3	GRADING & DRAINAGE PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CLP5.1	DETAILS	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CLP6.1	CROSS SECTIONS	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CULP1.0	PRIVATE & PUBLIC UTILITY PLAN COVER SHEET	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CULP2.1	UTILITY PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CULP2.2	UTILITY PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CULP2.3	UTILITY PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CSWMPLP1.0	STORM WATER MANAGEMENT PLAN COVER SHEET	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
CSWMPLP2.1	STORM WATER MANAGEMENT PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CSWMPLP2.2	STORM WATER MANAGEMENT PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CSWMPLP2.3	STORM WATER MANAGEMENT PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CILP1.0	FLOOD IRRIGATION PLAN COVER SHEET	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CILP2.1	FLOOD IRRIGATION PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CSWMPLP3.1	DETAILS	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CPLP1.0	OFF-SITE PAVING PLAN COVER SHEET	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CPLP1.1	OFF-SITE PAVING PLAN NOTES	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CPLP2.1	OFF-SITE PAVING PLAN DEMOLITION PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CPLP2.2	OFF-SITE PAVING PLAN DEMOLITION PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CPLP2.3	OFF-SITE PAVING PLAN DEMOLITION PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CPLP3.1	OFF-SITE PAVING PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CPLP3.2	OFF-SITE PAVING PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CPLP3.3	OFF-SITE PAVING PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CPLP4.1	OFF-SITE PAVING PLAN GRADING & DRAINAGE PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CPLP4.2	OFF-SITE PAVING PLAN GRADING & DRAINAGE PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
CPLP4.3	OFF-SITE PAVING PLAN GRADING & DRAINAGE PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
19th St Linear Park - Electrical					
SE1.1L	SITE ELECTRICAL COVER SHEET	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
SE2.1L	SITE ELECTRICAL PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
SE2.2L	SITE ELECTRICAL PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
SE2.3L	SITE ELECTRICAL PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
SE3.1L	SITE ELECTRICAL DETAILS	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
SE3.2L	SITE ELECTRICAL DETAILS	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
SE4.1L	PHOTOMETRIC ANALYSIS	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
SE4.2L	PHOTOMETRIC ANALYSIS	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
SE4.3L	PHOTOMETRIC ANALYSIS	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
19th St Linear Park - Street Lights					
SL1-L	STREET LIGHT COVER SHEET	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
SL2-L	STREET LIGHT PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
SL3-L	STREET LIGHT DETAILS	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
19th St Linear Park - Landscape					
LA-100BL	LANDSCAPE NOTES, LEGEND & KEY MAP	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
LA-101L	HARDSCAPE PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
LA-102L	HARDSCAPE PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
LA-103L	HARDSCAPE PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
LA-201L	HARDSCAPE DETAILS	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
LA-202L	HARDSCAPE DETAILS	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
LA-203L	HARDSCAPE DETAILS	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
LA-204L	HARDSCAPE DETAILS	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
LA-205L	HARDSCAPE DETAILS	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
LA-206L	HARDSCAPE DETAILS	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
LA-301L	LANDSCAPE PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
LA-302L	LANDSCAPE PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
LA-303L	LANDSCAPE PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
LA-401L	C.O.P. STANDARD DETAILS	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
LA-402L	LANDSCAPE DETAILS	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
LA-500L	IRRIGATION SCHEDULE	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
LA-501L	IRRIGATION PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
LA-502L	IRRIGATION PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
LA-503L	IRRIGATION PLAN	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
LA-601L	IRRIGATION DETAILS	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
LA-602L	IRRIGATION DETAILS	0	08/13/2025	08/22/2025	19th Street Linear Park Bid Set 8-13-25 (08/13/25)
Edison Park - General					
G001	COVER PAGE	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
Edison Park - Civil					
CEPE1.0	COVER-SITE GRADING & DRAINAGE COVER SHEET	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CEPE1.1	ON-SITE GRADING & DRAINAGE NOTES	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CEPE2.1	DEMOLITION PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CEPE2.2	DEMOLITION PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CEPE2.3	DEMOLITION PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CEPE2.4	DEMOLITION PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CEPE3.1	HORIZONTAL CONTROL PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CEPE3.2	HORIZONTAL CONTROL PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CEPE3.3	HORIZONTAL CONTROL PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CEPE3.4	HORIZONTAL CONTROL PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CEPE4.1	GRADING & DRAINAGE PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CEPE4.2	GRADING & DRAINAGE PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CEPE4.3	GRADING & DRAINAGE PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
CEPE4.4	GRADING & DRAINAGE PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CEPE5.1	DETAILS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CEPE6.1	CROSS SECTIONS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CSWMPEPE1.0	STORM WATER MANAGEMENT PLAN COVER SHEET	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CSWMPEPE2.1	STORM WATER MANAGEMENT PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CSWMPEPE2.2	STORM WATER MANAGEMENT PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CSWMPEPE2.3	STORM WATER MANAGEMENT PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CSWMPEPE2.4	STORM WATER MANAGEMENT PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CSWMPEPE3.1	STORM WATER MANAGEMENT PLAN DETAILS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CUEPE1.0	ON-SITE UTILITY PLAN COVER SHEET	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CUEPE1.1	ON-SITE UTILITY PLAN NOTES	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
CUEPE1.2	UTILITY PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
Edison Park - Site Electrical					
SE1.1	SITE ELECTRICAL COVER SHEET	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
SE2.1	SITE ELECTRICAL COVER SHEET	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
SE2.2	SITE ELECTRICAL LEGEND & LIGHT FIXTURE SCHEDULE	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
SE3.1	SITE ELECTRICAL DETAILS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
SE3.2	SITE ELECTRICAL DETAILS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
SE3.3	SITE ELECTRICAL DETAILS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
SE4.1	PHOTOMETRIC ANALYSIS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
SE4.2	PHOTOMETRIC ANALYSIS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
SE4.3	PHOTOMETRIC ANALYSIS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
SE5.1	PHOTOMETRIC ANALYSIS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
Edison Park - Street Lights					
SL1	STREET LIGHT COVER SHEET	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
SL2	STREET LIGHT PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
SL3	STREET LIGHT DETAILS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
Edison Park - Splash Pad					
SP-001	SPLASH PAD COVER SHEET	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
SP-002	SPLASH PAD SITE PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
SP-101	SPLASH PAD PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
SP-111	SPLASH PAD PLUMBING	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
SP-301	SPLASH PAD SECTIONS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
SP-601	SPLASH PAD SECTIONS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
SP-602	ELECTRICAL SCHEMATIC	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
Edison Park - Landscape					
LA-100A	LANDSCAPE TREE INVENTORY/SALVAGE LEGEND	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-100B	LANDSCAPE NOTES, LEGEND & KEY MAP	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-100B.1	LANDSCAPE TREE INVENTORY/SALVAGE	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-101	HARDSCAPE PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-102	HARDSCAPE PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-103	HARDSCAPE PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-104	HARDSCAPE PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-201	HARDSCAPE DETAILS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-202	HARDSCAPE DETAILS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-203	HARDSCAPE DETAILS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-204	HARDSCAPE DETAILS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
					8-13-25 (08/13/25)
LA-205	HARDSCAPE DETAILS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-206	HARDSCAPE DETAILS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-207	HARDSCAPE DETAILS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-208	HARDSCAPE DETAILS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-301	LANDSCAPE PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-302	LANDSCAPE PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-303	LANDSCAPE PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-304	LANDSCAPE PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-401	C.O.P. STANDARD DETAILS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-402	LANDSCAPE DETAILS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-500	IRRIGATION SCHEDULE	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-501	IRRIGATION PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-502	IRRIGATION PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-503	IRRIGATION PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-504	IRRIGATION PLAN	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-601	IRRIGATION DETAILS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)
LA-602	IRRIGATION DETAILS	0	08/13/2025	08/22/2025	Edison Park Improvement Bid Set 8-13-25 (08/13/25)

Current Specifications

Number	Description	Revision	Issued Date	Received Date	Set
100 - General Information					
GI-01	Edison Park Improvement - Linear Park Development IFB	0	12/22/25	10/27/25	Edison Park Improvement - Linear Park Development IFB Proj No. AH50100070 CDBG
200 - Specifications					
TS-001	Technical Specifications	0	12/01/25	11/07/25	Technical Specifications 7-2025
300 - Geotechnical Reports					
GR-01	Linear Park SEC 19th St & Villa Geotechnical Report Speedie & Assoc	0	12/22/25	10/27/25	Geotech Report - Linear Park SEC 19th St & Villa
GR-02	Vann Engineering NWC Villa St & 20th Street	0	12/22/25	10/27/25	Vann Engineering NWC Villa St and 20th Street - Portion of APN 116-11-001F
400 - Davis Bacon Wage Determination					
DB-01	City of Phoenix Davis Bacon Overview	0	12/22/25	12/11/25	City of Phoenix - Davis Bacon Overview
DB-02	Davis Bacon Wage Determination	0	12/22/25	10/27/25	Davis Bacon Wage Determination
500 - City of Phoenix Housing Department - Section 3					
01	City of Phoenix - Section 3 Requirements	0	12/22/25	12/11/25	City of Phoenix - Section 3 Requirements
02	Section 3 Contractor Book City of Phoenix	0	12/22/25	10/27/25	Section 3 Contractor Book - City of Phoenix
03	City of Phoenix - HUD 4010 Labor Standards	0	12/22/25	10/27/25	City of Phoenix - HUD 4010 Labor Standards
600 - Addendums					
AD-01	Addendum No. 2 EP- LPD	0	12/22/25	10/27/25	Addendum No. 2
700 - SRPMIC Cultural Sensitivity Training					
1	SRPMIC Cultural Sensitivity Training	0	12/22/25	12/11/25	SRPMIC Cultural Sensitivity Training

EXHIBIT E

See Specifications in Procore **Section 500 - City of Phoenix Housing Department - Section 3** for Section 3 requirements. See required forms to submit, beginning next page.



City of Phoenix

Section 3 Business Concern Certification for Contracting

Instructions: Enter the following information and select the criteria that applies to certify your Section 3 Business Concern* status.

Business Information

Project Name:			
Name of Business:			
Address of Business:			
Business Owner:			
Preferred Contact:			
Phone Number:		Email Address:	
Business Type:	☐ Corporation ☐ Partnership ☐ Sole Proprietorship ☐ Joint Venture		

Select from ONE of the following options below that applies:

- ☐ At least 51 percent of the business is owned and controlled by low- or very low-income persons.
- ☐ At least 51 percent of the business is owned and controlled by current public housing residents or residents who currently live in Section 8-assisted housing.
- ☐ Over 75 percent of the labor hours performed for the business over the prior three-month period are performed by Section 3 workers.
- ☐ Not a Section 3 Business Concern.

Affirmation

I affirm that the above statements are true, complete, and correct to the best of my knowledge and belief. I understand that businesses who misrepresent themselves as Section 3 business concerns and report false information to City of Phoenix may have their contracts terminated as default and be barred from ongoing and future considerations for contracting opportunities. I hereby certify**, under penalty of law, that the following information is correct to the best of my knowledge.

Additionally, I affirm that I have read and understand the HUD Section 3 requirements and responsibilities listed in the Section 3 Clause (24 CFR 75).

Print Name: _____ Signature: _____

Date: _____

FOR ADMINISTRATIVE USE ONLY

Is the business a Section 3 business concern based upon their certification? YES NO

*Information regarding Section 3 Business Concerns can be found at 24 CFR 75.5.

**Certification expires within six months of the date of signature.

EMPLOYERS MUST RETAIN THIS FORM IN THEIR SECTION 3 COMPLIANCE FILE FOR FIVE YEARS.





City of Phoenix

Section 3 Worker and Targeted Section 3 Worker Self-Certification

The purpose of HUD's Section 3 program is to provide employment, training, and contracting opportunities to low-income individuals, particularly those who are recipients of government assistance for housing or other public assistance programs. Your response is voluntary, confidential, and has no effect on your employment. A Section 3 worker seeking certification shall self-certify and submit this form to the recipient contractor or subcontractor, that the person is a Section 3 worker or Targeted Section 3 Worker as defined in 24 CFR Part 75.

Eligibility for Section 3 Worker or Targeted Section 3 Worker Status

Instructions: Enter/select the appropriate information to confirm your Section 3 worker or Targeted Section 3 Worker status.

Name:		Hire Date	
Address:			
Are you a resident of public housing or a Choice Neighborhoods?		☐ YES	☐ NO
Are you a resident of the City of Phoenix?		☐ YES	☐ NO
Is your individual income equal to or less than \$49,500 per year?		☐ YES	☐ NO
Do you live within 1 mile of the project site(s)?		☐ YES	☐ NO

Employee Affirmation

I affirm that the above statements are true, complete, and correct to the best of my knowledge and belief. I hereby certify, under penalty of law, that the following information is correct to the best of my knowledge.

Print Name: _____ Signature: _____

Date: _____

FOR ADMINISTRATIVE USE ONLY			
Is the employee a Section 3 worker based upon their self-certification?		☐ YES	☐ NO
Is the employee a Targeted Section 3 worker based upon their self-certification?		☐ YES	☐ NO
Was this an applicant who was hired as a result of the Section 3 project?		☐ YES	☐ NO
If yes, Name of Company		Hire Date:	

EMPLOYERS MUST RETAIN THIS FORM IN THEIR SECTION 3 COMPLIANCE FILE FOR FIVE YEARS.





Ciudad de Phoenix

Autocertificación del trabajador de la Sección 3 y del trabajador de la Sección 3 con estatus específico

El propósito del programa de la Sección 3 de HUD es brindar oportunidades de empleo, capacitación y contratación a personas de bajos ingresos, en particular a quienes reciben asistencia del gobierno para vivienda u otros programas de asistencia pública. Su respuesta es voluntaria, confidencial y no tiene ningún efecto sobre su empleo. Un trabajador de la Sección 3 que busque la certificación deberá autocertificarse y enviar este formulario al contratista o subcontratista receptor, de que la persona es un trabajador de la Sección 3 o un Trabajador de la Sección 3 con estatus específico como se define en 24 CFR Parte 75.

Instrucciones para elegibilidad de trabajador de la Sección 3 o trabajador de la Sección 3 con estatus específico. Ingrese/seleccione la información adecuada para confirmar su estado de trabajador de la Sección 3 o Trabajador de la Sección 3 con estatus específico

Nombre		Fecha de Inicio	
Dirección			
¿Es usted residente de una vivienda pública o de una elección de vivienda?	☐ SI	☐ NO	
¿Es usted residente de la Ciudad de Phoenix?	☐ SI	☐ NO	
¿Su ingreso individual es igual o menor a \$49,500 por año?	☐ SI	☐ NO	
¿Vive dentro de 1 milla del sitio(s) del proyecto?	☐ SI	☐ NO	

Afirmación del Empleado

Afirmo que las declaraciones anteriores son verdaderas, completas y correctas a mi leal saber y entender. Por la presente certifico, bajo pena de ley, que la siguiente información es correcta a mi leal saber y entender.

Nombre : _____

Firma : _____

Fecha: _____

SOLO PARA USO ADMINISTRATIVO			
¿Es el empleado un trabajador de la Sección 3 según su autocertificación?		☐ SI	☐ NO
¿Es el empleado un trabajador de la Sección 3 con estatus específico en función de su autocertificación?		☐ SI	☐ NO
¿Era este un solicitante que fue contratado como resultado del proyecto de la Sección 3?		☐ SI	☐ NO
Si es así nombre de la Empresa		Fecha de Contratación	

LOS EMPLEADORES DEBEN CONSERVAR ESTE FORMULARIO EN SU ARCHIVO DE CUMPLIMIENTO DE SECCIÓN 3 DURANTE CINCO AÑOS



This page intentionally left blank.

END OF EXHIBIT E



Arizona Department of Revenue

Arizona Form
5005

Contractor's Certificate Prime Contracting and MRRA

The purpose of this Certificate is to provide a subcontractor with the validation required for prime contracting transaction privilege tax (TPT) exemption, and for exemption from liability for an amount equal to retail TPT on materials incorporated or fabricated into maintenance, repair, replacement or alteration (MRRA) projects. The Certificate can be provided for a particular project, for a period of time, or until revoked. This Certificate establishes liability of the contractor issuing it for the prime contracting TPT and/or the amount equal to the retail TPT; therefore, it must be completed by the contractor assuming the liability. The asterisked (*) items must be completed; otherwise, the Certificate is not valid. The Department may disregard this Certificate pursuant to A.R.S. § 42-5008.01 or A.R.S. § 42-5075.E if the Certificate is incomplete or erroneous. If disregarded, the subcontractor accepting the Certificate will have the burden of proving (pursuant to A.R.S. § 42-5008.01 or A.R.S. § 42-5075.D), that it is not liable for the prime contracting TPT and/or the amount equal to the retail TPT.

Prime contractor should provide this Certificate to the subcontractor(s) and retain a copy for their records.

A. Contractor

* Name Low Mountain Construction, Inc.	* ☒ TPT License ☐ Tribal Business License ☐ Tribal Number 07-435384 P		
* Address 4105 N. 20th Street, Suite 205	City, Town or Post Office Phoenix	State AZ	ZIP Code 85016
AZ Contractor License Number ROC 094132 B	Phone Number (602) 265-2201		
☐ I am a Native American Contractor working on the reservation established for my tribe. (Provide your Tribal Business License or Tribal Number above.)			
I am performing contracting work for a ☐ Native American member or ☐ the Tribe for which the reservation is established named below. Name of Tribe			

B. Subcontractor

* Name	* TPT License # (if none, write "N/A - MRRA only")		
* Address	City, Town or Post Office	State	ZIP Code
AZ Contractor License Number	Phone Number		

C*. Type of Certificate (check one and provide requested information)

☒ Single Project Certificate *PROJECT DESCRIPTION * (For example; Building Permit #, Address, Subdivision, Book/Map/Parcel #s, and/or Legal Description) 25470 Edison and Linear Park; 901 N 19th Street and 1940 E Villa Street, on portions of parcels 116-10-055D and 116-11-001F, Phoenix, AZ 85006 Project Designation (see instructions for definitions) ☐ MRRA ☐ Modification	OR	☐ Blanket Certificate (check applicable box and fill in requested information). ☐ Period From: _____ Through: _____ ☐ Until revoked * NOTE: Blanket Certificate indicates the prime contractor is responsible for every contract during the period regardless of contract designation. ☐ Specific Project Exclusion: ☐ Description: _____ Designation: ☐ MRRA ☐ Modification
--	----	---

I hereby certify that I am the contractor issuing this form or I have authority to sign this Certificate on behalf of Contractor. I understand that by executing this Certificate, Contractor is licensed for TPT purposes and is assuming the prime contracting TPT liability and/or the amount equal to retail TPT liability applicable to the above referenced project(s).

Tyra Renshaw

SIGNATURE

Director - Preconstruction I Contracts

TITLE

Digitally signed by Tyra Renshaw
Date: 2025.12.23 09:44:48 -07'00'

Tyra Renshaw

PRINT NAME

12/23/2025

DATE SIGNED

PROJECT: 25470 EDISON AND LINEAR PARK**NAME & LOCATION**

Edison and Linear Park

901 N 19th Street and 1940 E Villa Street, on portions of parcels 116-10-055D and 116-11-001F
Phoenix, AZ 85006

OWNER

City of Phoenix
200 W Washington St
Phoenix, AZ 85003

GENERAL CONTRACTOR

Low Mountain Construction, Inc.
4105 North 20th Street, Suite 205
Phoenix, AZ 85016

PROJECT NO.

25470

BOND NO.

101639531

SURETY COMPANY

Merchants National Bonding Inc.
6700 Westown Parkway
West Des Moines, IA 50266

AGENT

Bonding Solutions LLC
1635 N Greenfield Rd, Suite 127
Mesa, AZ 85205
480.835.6745

COMPANY CONTACTS

Your Company Name: _____

Project: **25470 EDISON AND LINEAR PARK**

Please provide us with the appropriate contacts for this **specific** job in the directory log chart below. Points of contact needed include:

- ✦ Invoicing
- ✦ Contract Documentation
- ✦ Superintendent
- ✦ Estimator
- ✦ Foreman
- ✦ Other—*Anyone else that may be an essential contact on this project*

JOB TITLE	NAME	EMAIL	PHONE NUMBER
			*Please add cell # if primarily on jobsite

 Please submit this form to trenshaw@lowmountain.com

SUPPLIER LIST

Your Company Name: _____

Project: 25470 EDISON AND LINEAR PARK

LIST OF VENDORS SUPPLYING MATERIAL/WORK ON THIS PROJECT

Please list all of your suppliers below:

☐ There are **NO SUPPLIERS** on this project.

▶▶▶ Please submit this form to apatton@lowmountain.com

PROJECT: 25470 EDISON AND LINEAR PARK

For your reference and ease of submitting all documents needed for this project, please find below a checklist of items to be submitted to trenshaw@lowmountain.com, apatton@lowmountain.com, or to be entered in Procore as noted in the contract package.

✓	DOCUMENT:	SUBMIT TO:
	Signed Exhibit A or PO and Master Contract, as applicable (Exhibit A or PO is accessible in your Procore Commitment > Export > PDF)	trenshaw@lowmountain.com
	Current W-9	apatton@lowmountain.com
	Project Specific Insurance Certificates (see Exhibit C)—Workman's Compensation, General Commercial Liability and Auto policies	apatton@lowmountain.com
	Subcontractor Schedule of Values (SSOV)	Enter in Procore
	Company Contacts	trenshaw@lowmountain.com
	Supplier List	apatton@lowmountain.com
	SRPMIC Cultural Sensitivity Training Tracker Excel file (Upon completion/receipt of CST Training Sticker)	City of Phoenix
	Submission of Weekly Safety Meeting Logs	jconover@lowmountain.com
	Submission of Weekly Payroll Reports	LCP Tracker
	Maricopa County Subcontractor Registration Confirmation	apatton@lowmountain.com
	Section 3 Forms - Business Concern Certification for Contracting - Worker and Targeted Section 3 Worker Self-Certification	jconover@lowmountain.com
	ROC License	apatton@lowmountain.com
